# Update on Construction Closeout of the Salesforce Transit Center

May 14, 2020






## Contract Close out Status

### Trade Group status:

- 1 Trade Group in the Full & Final change order process
- 12 Trade Groups proceeding to Dispute Resolution
- 36 Trade Groups are closed out

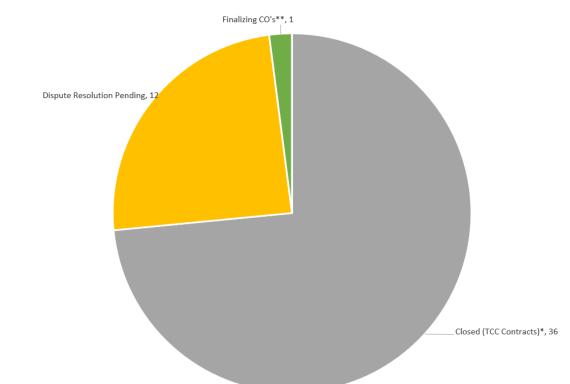

<sup>\*\*\*</sup> Full & Final Executed awaits final retention and billing to close



<sup>\*</sup>Closed includes retention released and final billed

<sup>\*\*</sup>Finalizing CO's includes Girder Work Support Trades now work is complete.

## Contingency Cost

#### Contingency Tracking (\$millions)

	Construction Contingency	CM/GC Contingency	Program Reserve	Total Contingency & Reserve
Baseline Budget Amounts	\$61.8	\$32.5	\$117.0	\$211.3
Contingency Usage Through March 2020	(\$60.8)	(\$26.6)	(\$86.4)	(\$170.6)
Remaining Baseline Budget Amounts (at March 2020)	\$1.0	\$5.9	\$30.6	\$37.5
Total Draws/Adds April 2020	0.6	(0.4)	(0.0)	0.2
Remaining Balances	\$1.6	\$5.5	\$30.6	\$37.7

#### **Uses of Contingency this period**

Structural concrete various coordination issues, schedule mitigation and repairs; Dewatering well preparations, signage and K-Rail installation; Mission Street traction power preconstruction; and various other miscellaneous changes; Credit for unused bus ramp base bid allowance and unit price items.

#### **Forecasted Contingency Use**

CM/GC: \$1.9M

Construction: \$1.3M



## **Budget Status**

(\$millions)

	Current Budget		Estimate at Completion
Construction	1,534.8	1,523.7	1,548.2
Construction and CM/GC Contingencies	7.1	-	-
Design and Support Contracts	624.3	618.6	626.3
Phase 1 Target	2,166.2	2,142.3	2,174.5
Tenant Improvements	35.5	19.6	35.5
301 Mission Legal	27.1	21.2	27.1
Phase 1 Target with TI and 301M Legal	2,228.8	2,183.1	2,237.1
Program Reserve	30.6	-	22.3
Total Phase 1 Program	2,259.4	2,183.1	2,259.4
* Some March actuals are estimated			





# Thank You

