



Field Progress Update

December 9, 2010

Transbay Transit Center

TJPA





Transbay Transit Center

Field Progress Update

- Phase II and Phase III Demolition Work continues throughout the existing Terminal. This includes:
 - Over 20,000 craft hours without accident or incident
 - Continued Salvage Work
 - Continued Existing Terminal Building Abatement
 - Completed First Street Overpass Removal
 - Completed Removal of Bus Deck Roof and Walls
 - Started Central Terminal Building demolition with wrecking ball
- Initial Utility Relocation Package Trade Contractor began work. This includes:
 - Potholing to verify existing utilities on Minna and First Streets underway
 - Submittals and initial schedule for first package under review
- 301 Mission Street Temporary Wall
 - Preconstruction Meeting held with Webcor / Obayashi and Trade Contractor



Transbay Transit Center


Demolition Phasing

Phase 1 (16 days):
Aug 13, 2010 – Aug
28, 2010

Phase 2 (64 days):
Aug 29, 2010 – Nov
11, 2010

Phase 3 (120 days):
Nov 1, 2010 – Feb 28,
2011

Phase 4 (60 days):
Mar 1, 2011 – Apr 29,
2011

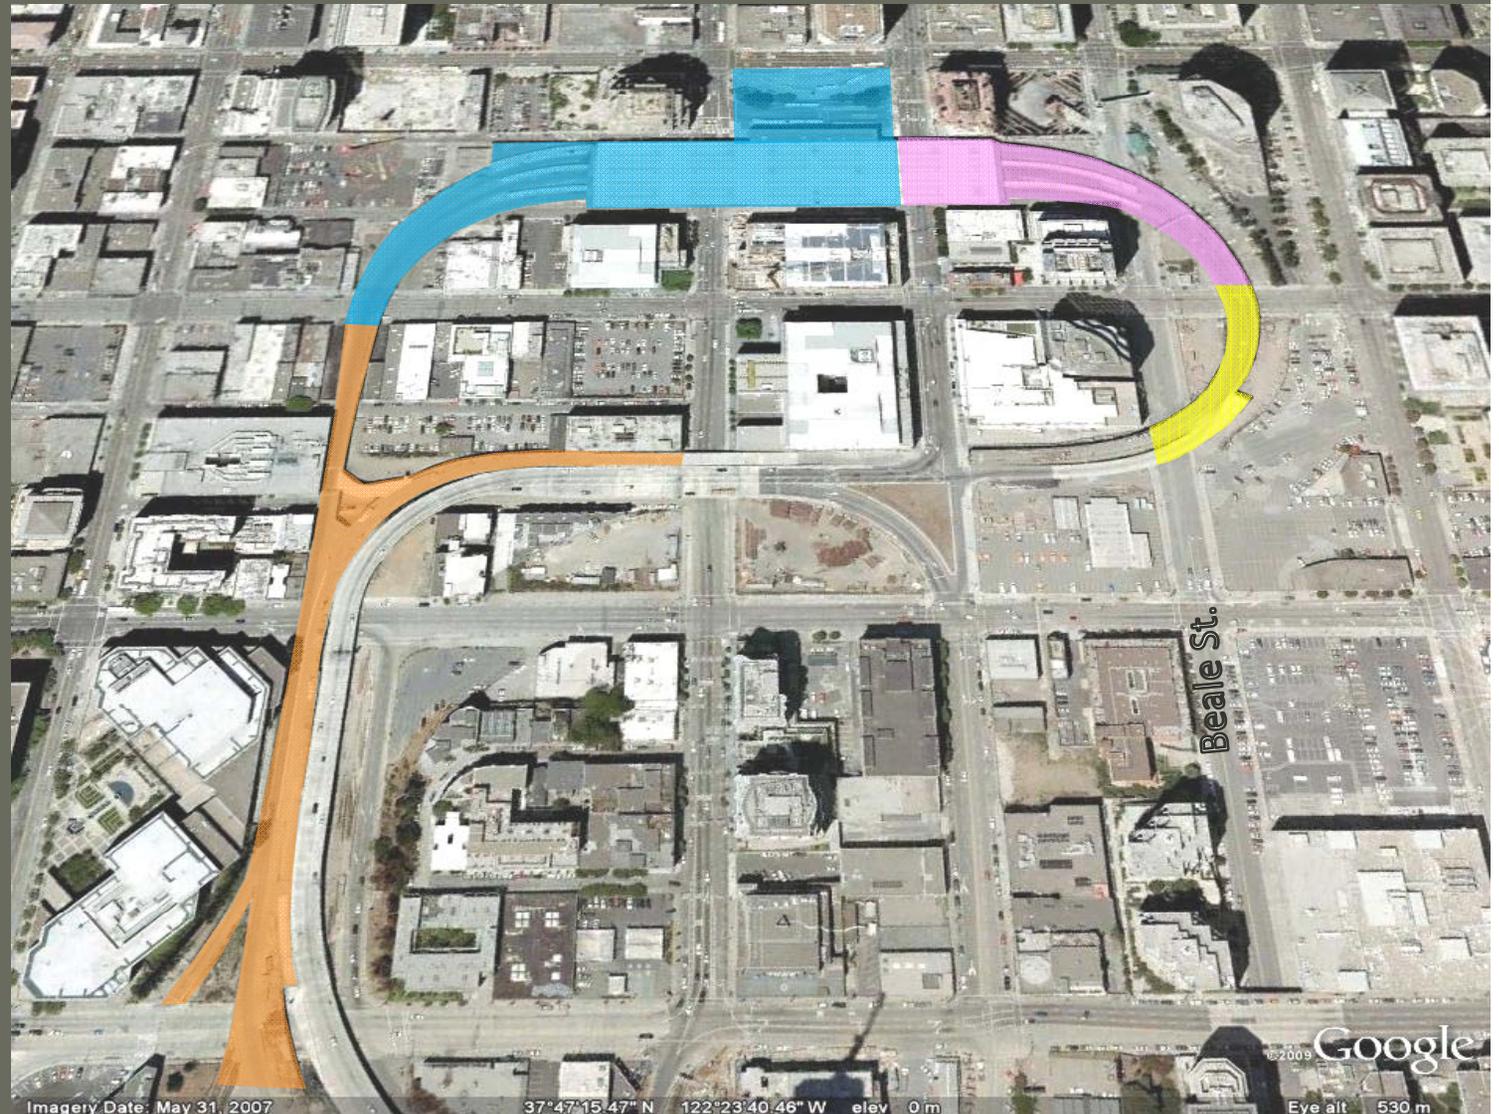

Imagery Date: May 31, 2007

37°47'15.47" N 122°23'40.46" W elev 0 m

Eye alt 530 m



Transbay Transit Center

Utility Relocation Trade Package Map

MISSION ST

Package TG04.2

Package TG04.6

MINNA ST

Package TG04.5.1

Package TG04.5.1

NATOMA ST

Package TG04.4

Package TG04.4

Package TG04.1

FIRST ST


FREMONT ST

BEALE ST

MAIN ST

HOWARD ST

Package TG04.3

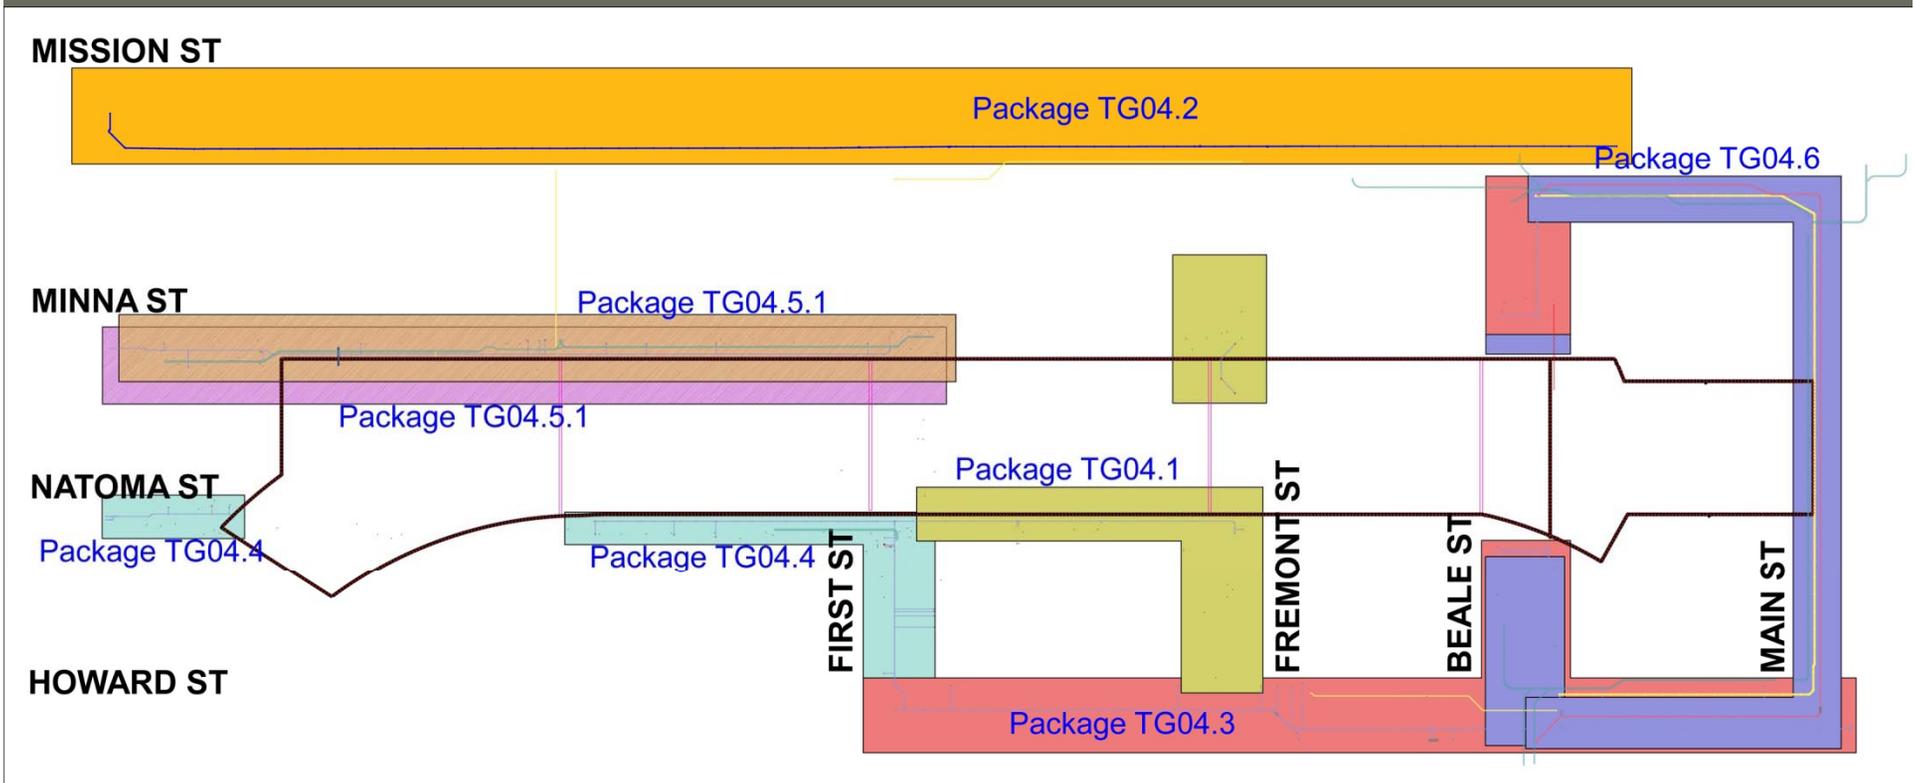



Transbay Transit Center

Salvaged Items - Benches





Transbay Transit Center

Demolition of Concrete Deck on First Street Overpass





Transbay Transit Center

Shearing the Steel at First Street Overpass





Transbay Transit Center

First Street Overpass Removed





Transbay Transit Center

Utility Relocation Began on Minna with Potholing





Transbay Transit Center

Utility Relocation Work in First Street





Transbay Transit Center

New Equipment Arrives





Transbay Transit Center

Central Terminal Demolition Begins





Transbay Transit Center

Central Terminal Demolition Begins





Transbay Transit Center

Bay Area Labor - Demolition

- To date, Evans Brothers, Inc. and their subcontractors have worked a total of:


20,564 Craft Hours

- To date, Bay Area Labor has contributed 19,172 hours, or 93.2% of the total Craft Hours completed on Phases I, II and III of the demolition.



Transbay Transit Center

Demolition Timeline Summary

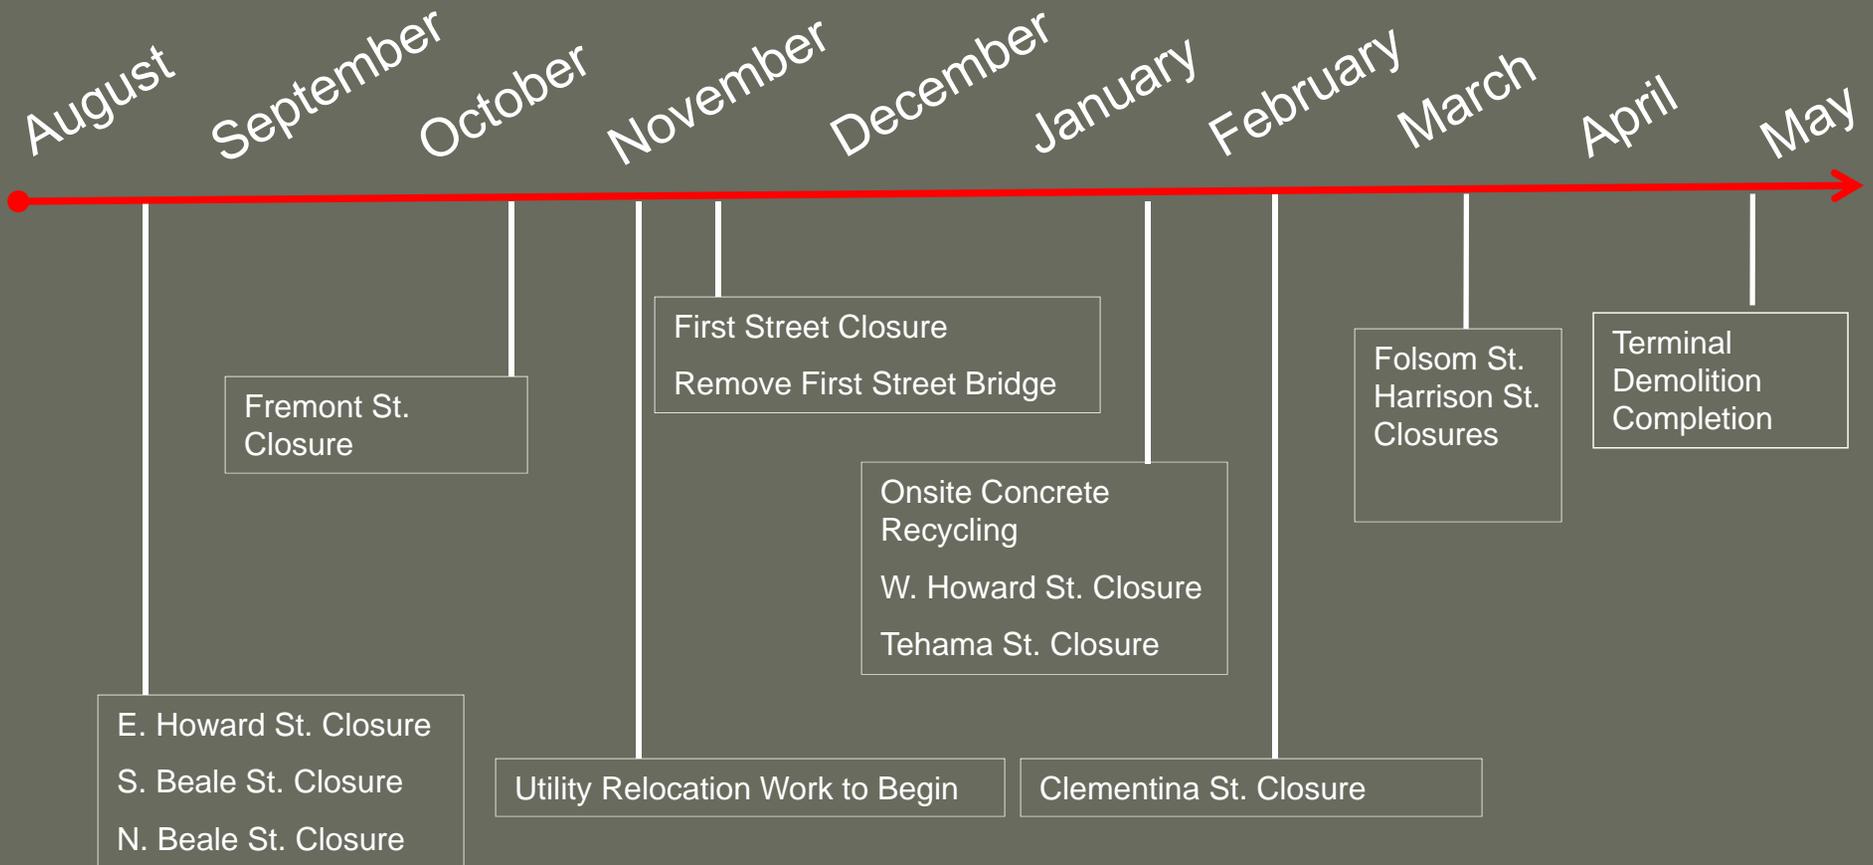



Transbay Transit Center

Utility Relocation Timeline Summary

