


Facility Readiness Update

March 2018



Facility Readiness – Lincoln Tenant Improvements

- Greyhound/Amtrak
 - Greyhound/Amtrak awarded: \$1.46M as compared to budget of \$1.69M
 - TJPA/Lincoln/Turner SPD & WOJV coordinating access
 - Completion May, however, pending WOJV
- Operational Areas
 - Mailroom finalizing equipment power needs followed by conversion to construction documents
 - TJPA/Lincoln office converting schematics to construction drawings nearly complete
 - Contract award about 3-4 weeks
- Permitting
 - TJPA deferring permitting authority to DBI for retail areas

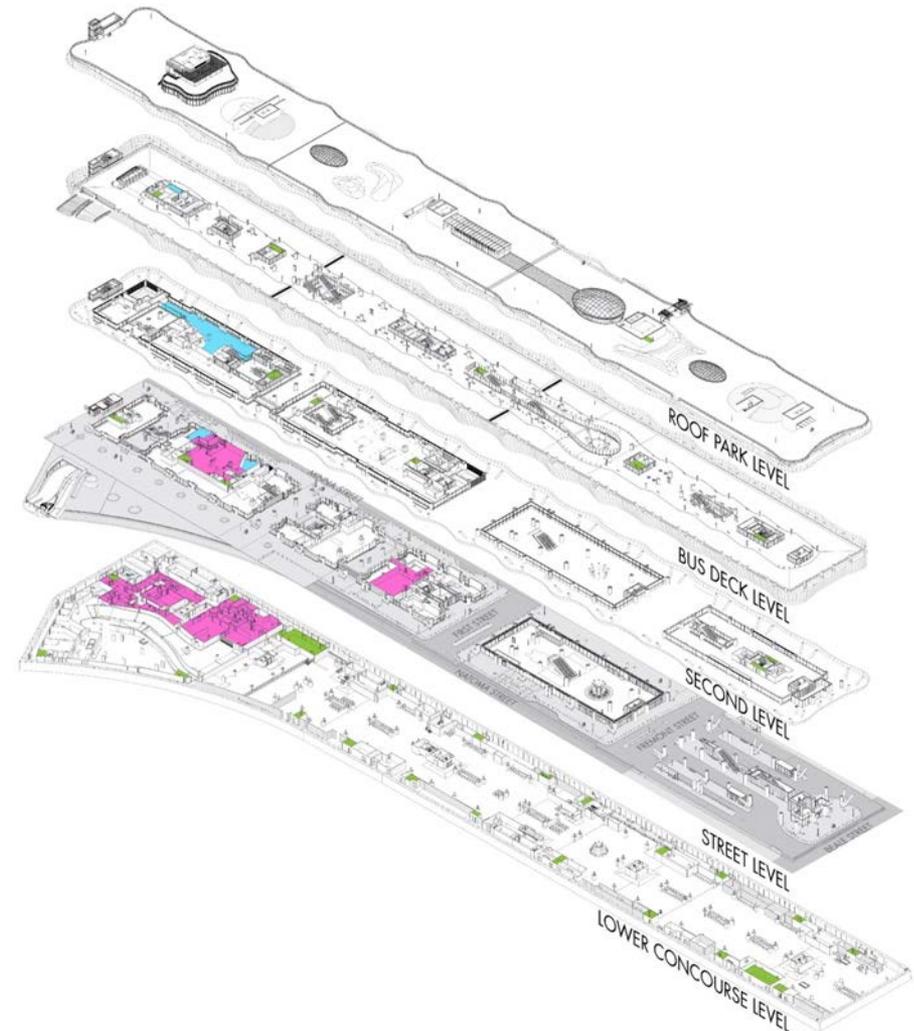

Facility Readiness – Lincoln Tenant Improvements

Amtrak/Greyhound


Budget: \$1,694,721

Low Bid: \$1,461,807

<u>Contract Work</u>	<u># of Bids</u>	<u>Low Bid</u>	<u>Mid Bid</u>	<u>High Bid</u>
Concrete - Topping Slab	3	\$ 80,849	\$ 133,342	\$ 153,823
Millwork	3	\$ 64,322	\$ 71,645	\$ 102,545
Doors, Frames, & Hardware	3	\$ 51,232	\$ 60,385	\$ 65,530
Glazing	3	\$ 34,401	\$ 74,091	\$ 75,000
Drywall	3	\$ 74,105	\$ 87,031	\$ 136,004
Tile	4	\$ 5,627	\$ 5,770	\$ 5,837
Accoustical Ceiling	4	\$ 35,887	\$ 41,843	\$ 42,185
Flooring	3	\$ 63,546	\$ 65,600	\$ 67,344
Toilet Partitions/Accessories	3	\$ 3,494	\$ 3,510	\$ 3,690
Fire Sprinklers	5	\$ 16,872	\$ 15,375	\$ 23,532
Plumbing	3	\$ 26,673	\$ 73,629	\$ 100,745
Painting	3	\$ 21,689	\$ 21,689	\$ 21,689
HVAC	5	\$ 183,931	\$ 221,240	\$ 329,434
Electrical	3	\$ 312,965	\$ 351,193	\$ 486,987
Total Primary Subcontractors	3	\$ 975,593	\$ 1,226,343	\$ 1,614,345
Other Expenses & Fees		\$ 486,214	\$ 553,249	\$ 656,978
Total Initial GMP Value		\$ 1,461,807	\$ 1,779,592	\$ 2,271,323


Facility Readiness – Lincoln Tenant Improvements

Path of travel

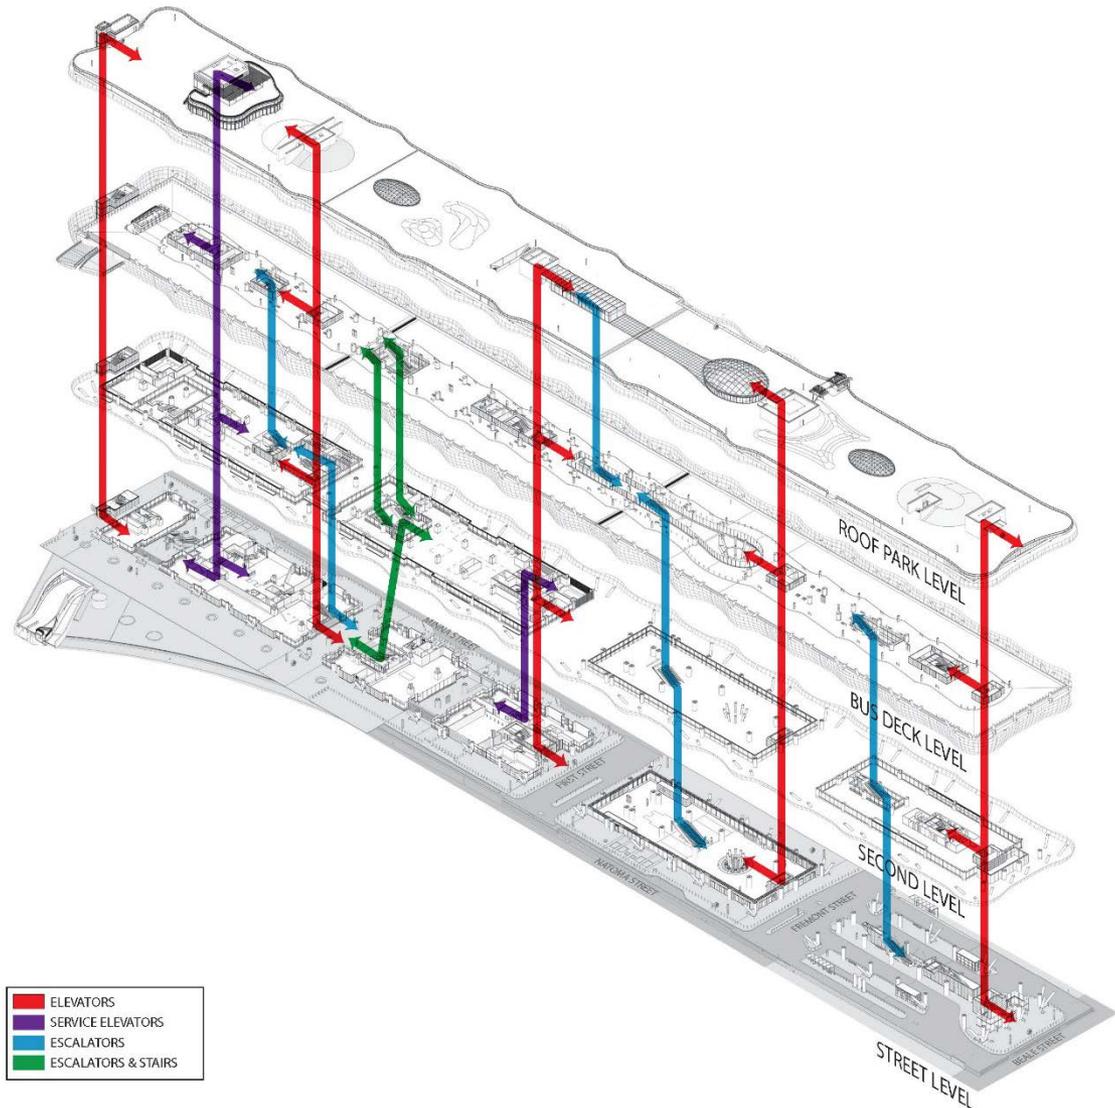


Facility Readiness – Lincoln Facility Maintenance

- Finalizing key contracts: marketing and promotion and CMMS
- Completing the other 25 priority service contracts by end of March; rest to follow per need
- Finalized equipment selections and procurement process
- Planning operating procedures and protocols
- WOJV dependent activities ongoing to include commissioning and O&M/Warranty deliverable

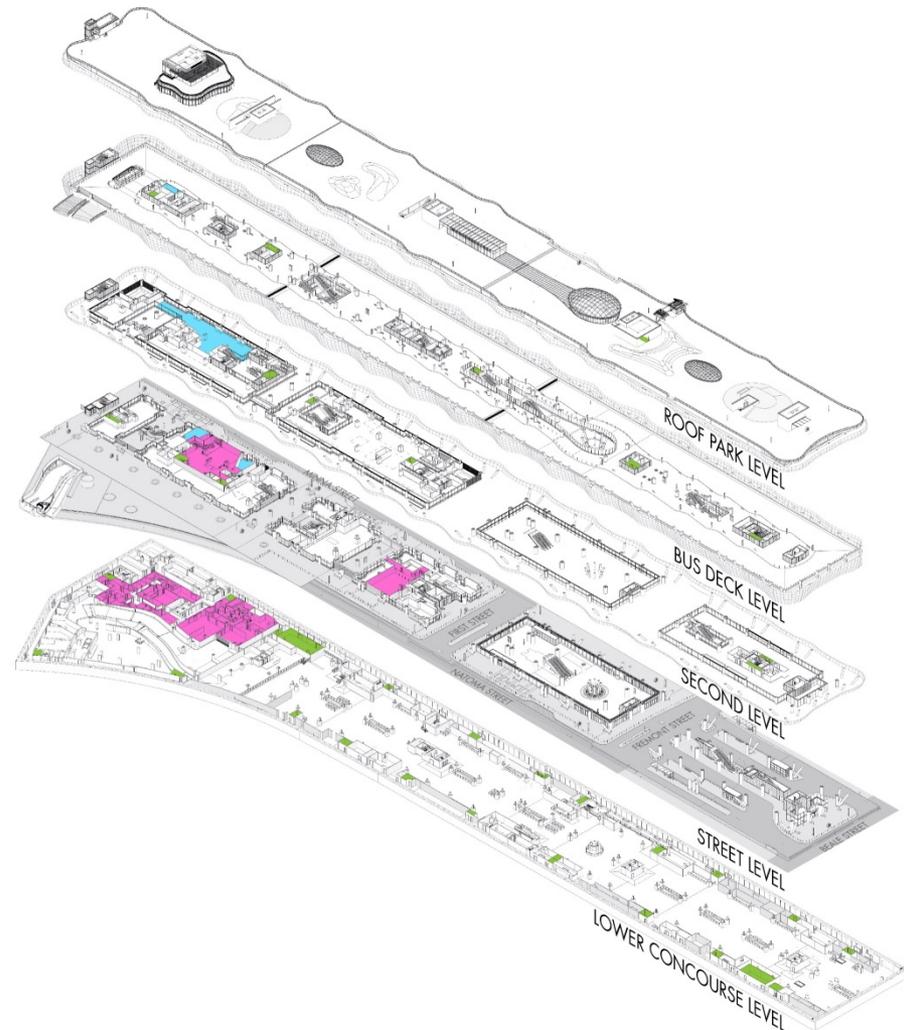


Facility Readiness – BRV Roof Park

- Finalizing initial programming and event calendars; pending opening date
- Finalizing park operational procedures: janitorial and landscaping
- Setting up procedural requirements for programming and events partners
- Revisiting Place of Entertainment framework; includes pricing menu
- Coordinating security program with Chief Security Officer pending opening date
- Solidifying initial bench of programming partners (approx. 15) pending opening date

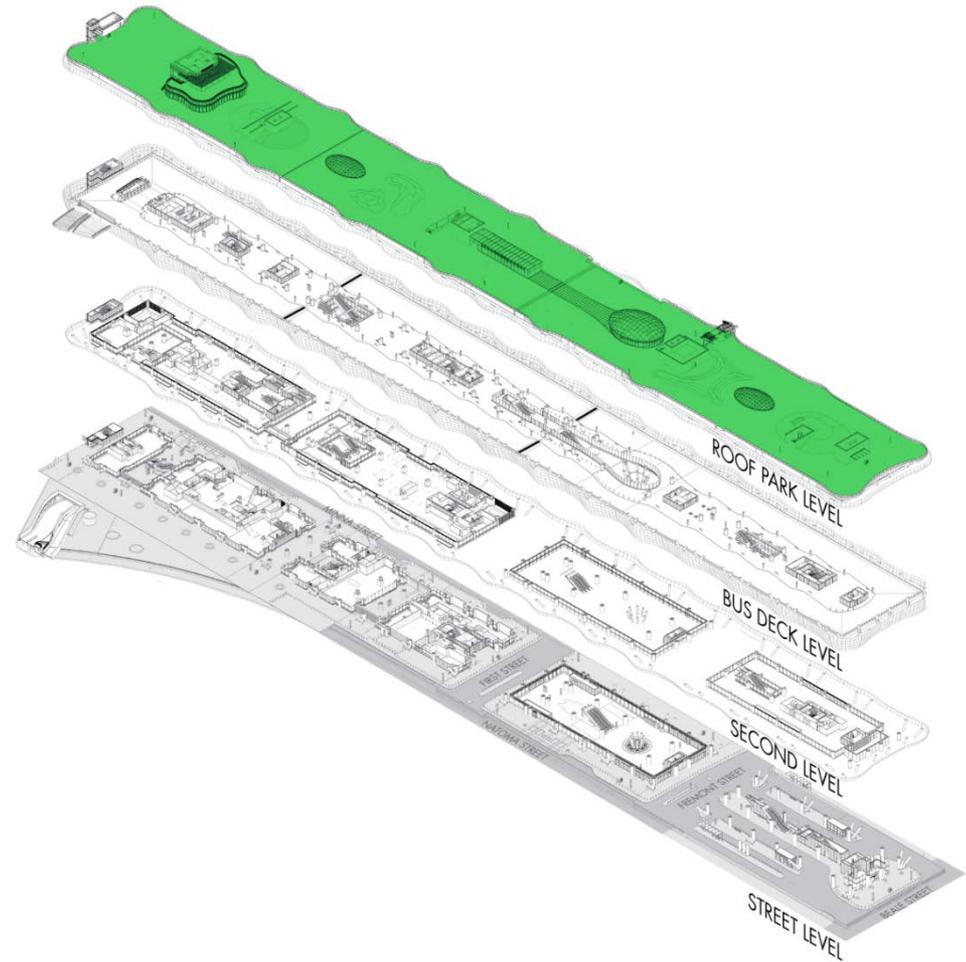

Facility Readiness – Pearl Digital Media


- Collaborating with transit operators and MTC-511 for transit information display is ongoing
- Sales packages being marketed
- Advertising sales are in process and campaigns will commence upon center opening
- Activating content management system pending receipt of media players by end of March triggering hardware and software testing, installation, further testing; dependent on WOJV installing and electrifying the kiosks
- Optimization planned for August

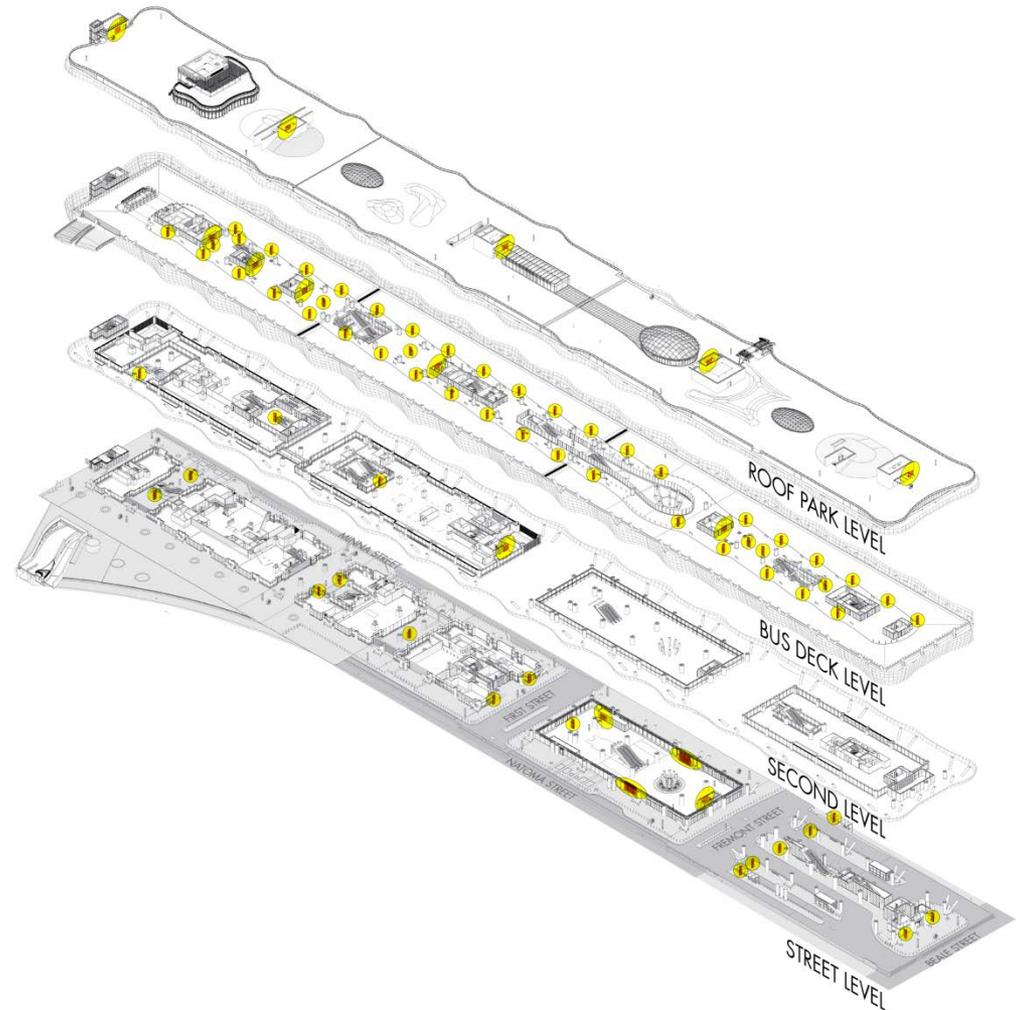

Facility Readiness – PRI Pop-Up Retail


PRI:

- Completed comprehensive plan to include revenue projections; final presentation to TJPA in March
- Continue to market pop-up spaces with ongoing coordination with BRV, Pearl, and Colliers
- Finalizing agreements pending solid opening date

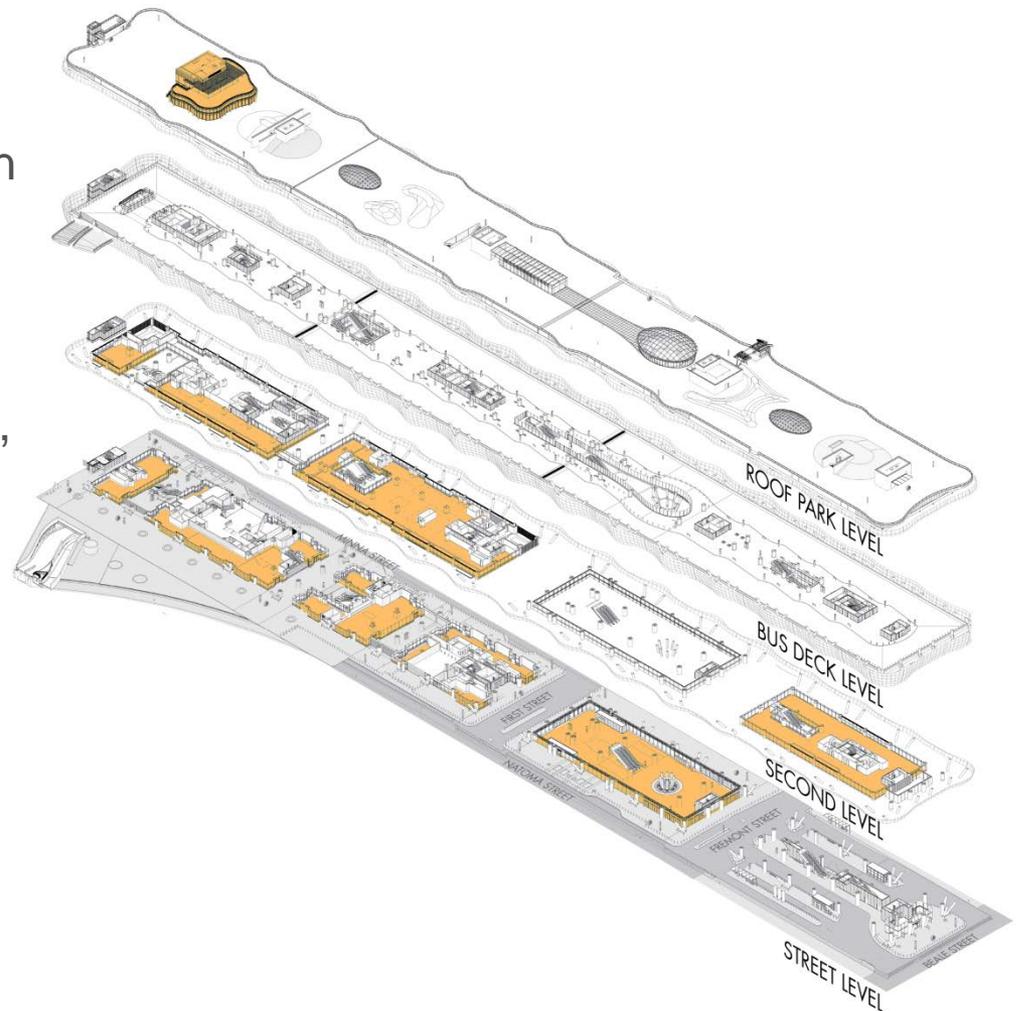


Facility Readiness - Transit

- Bus deck testing with AC Transit underway
- Developing driver training program
- Ongoing planning for vacating temporary terminal; dependent on center opening date
- SFMTA agreements for lease and ancillary agreements nearly complete; plan to go to SFMTA Board in April
- AC Transit personnel presented license agreement template for bus Deck to AC Transit Board in February
- Restarted talks Amtrak for 2nd floor

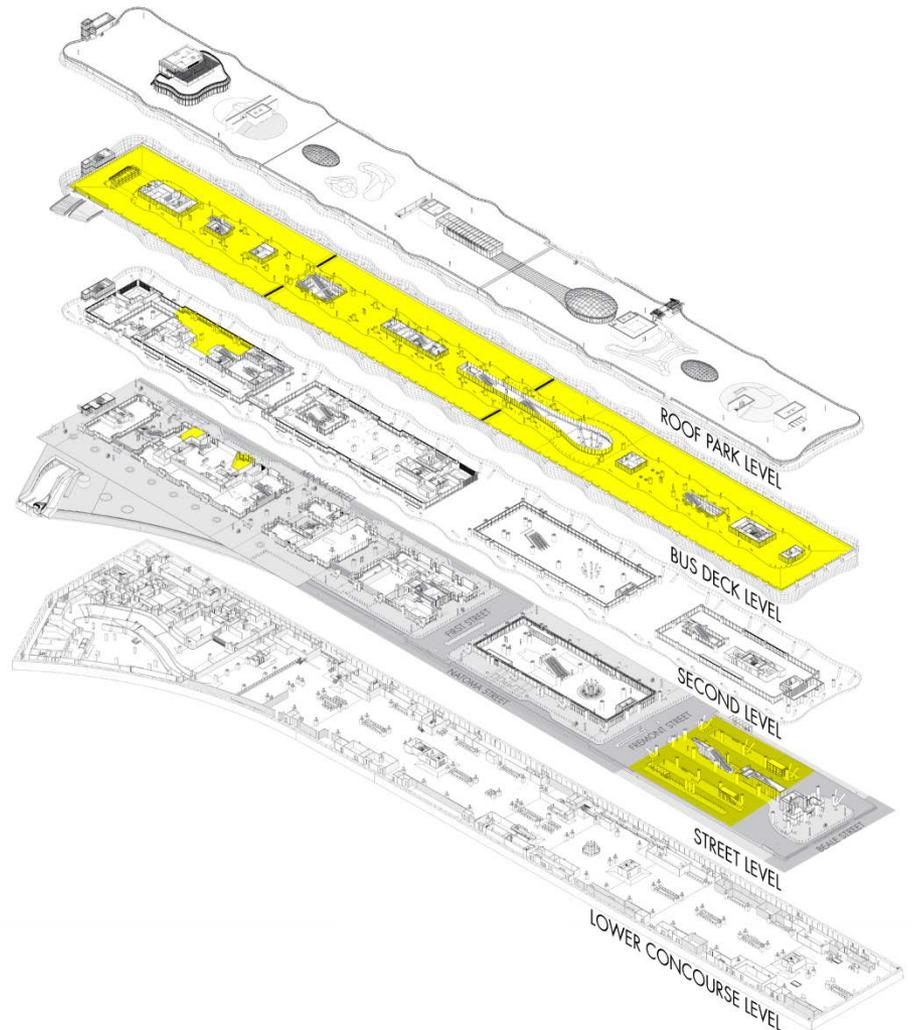


Schedule

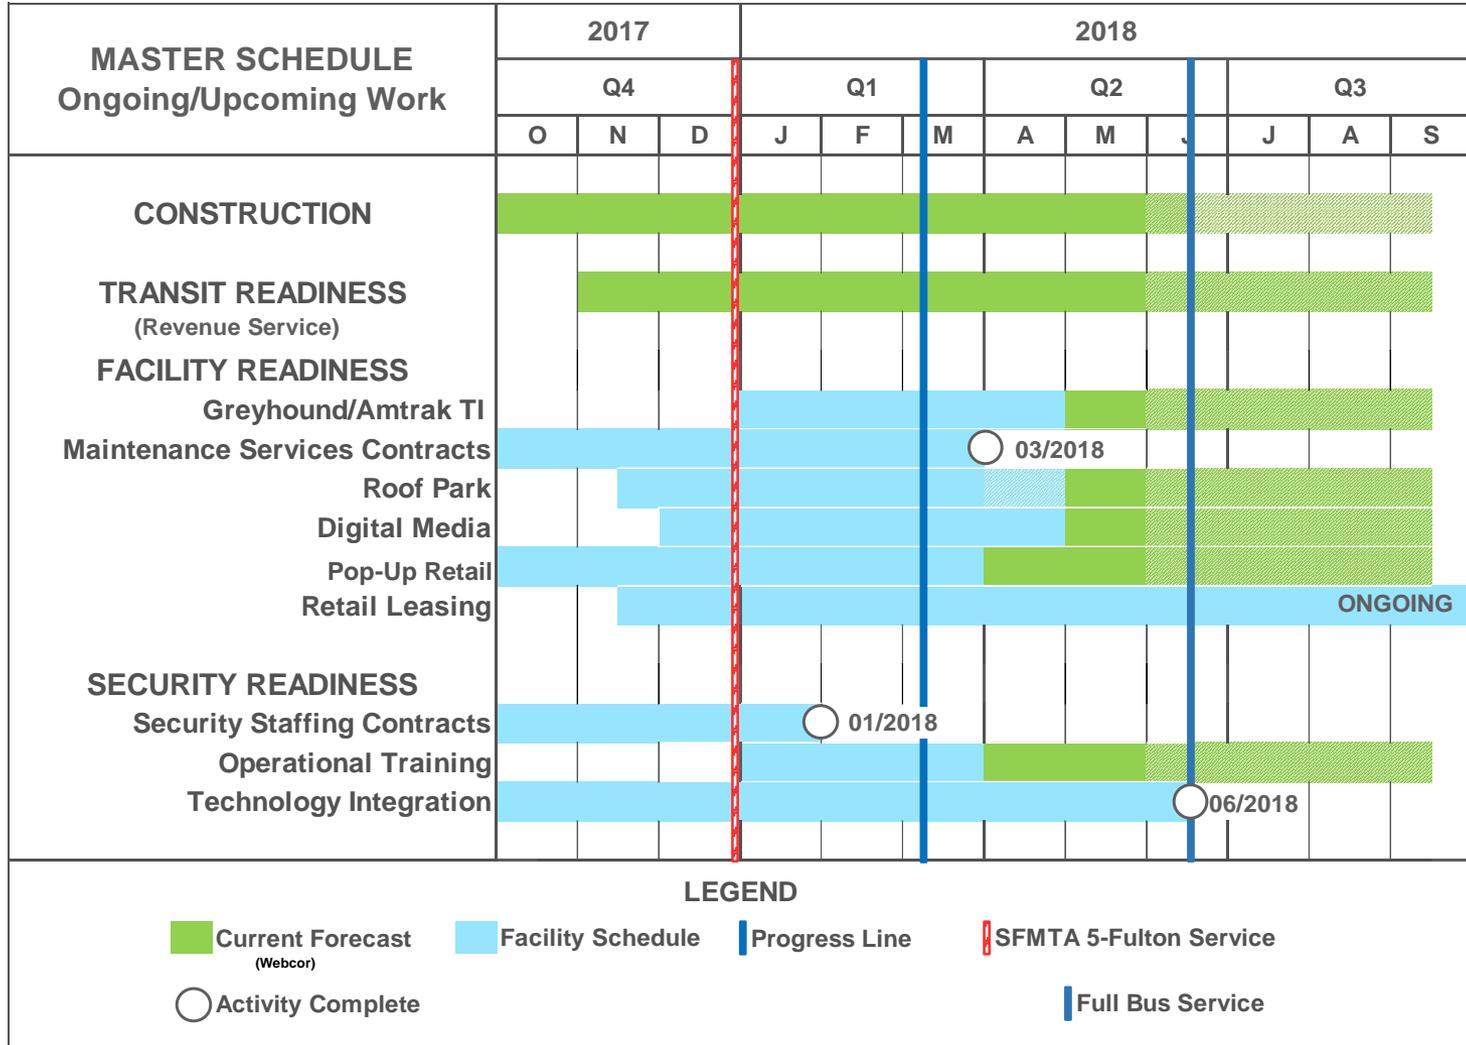

Facility Readiness - Security

- Code of Conduct presentation to Board during March meeting
- InfoSec/Cybersecurity contract presentation during March Board meeting
- Standard Operating Procedures are under development and will be in place prior to opening
- Pre-opening security training is on hold until 10 weeks prior to opening because hiring security staff too early will idle staff
- PSIM and ECS/MNS project will be complete in June 2018, provided the security team has access to the building, with operable security systems, in due time

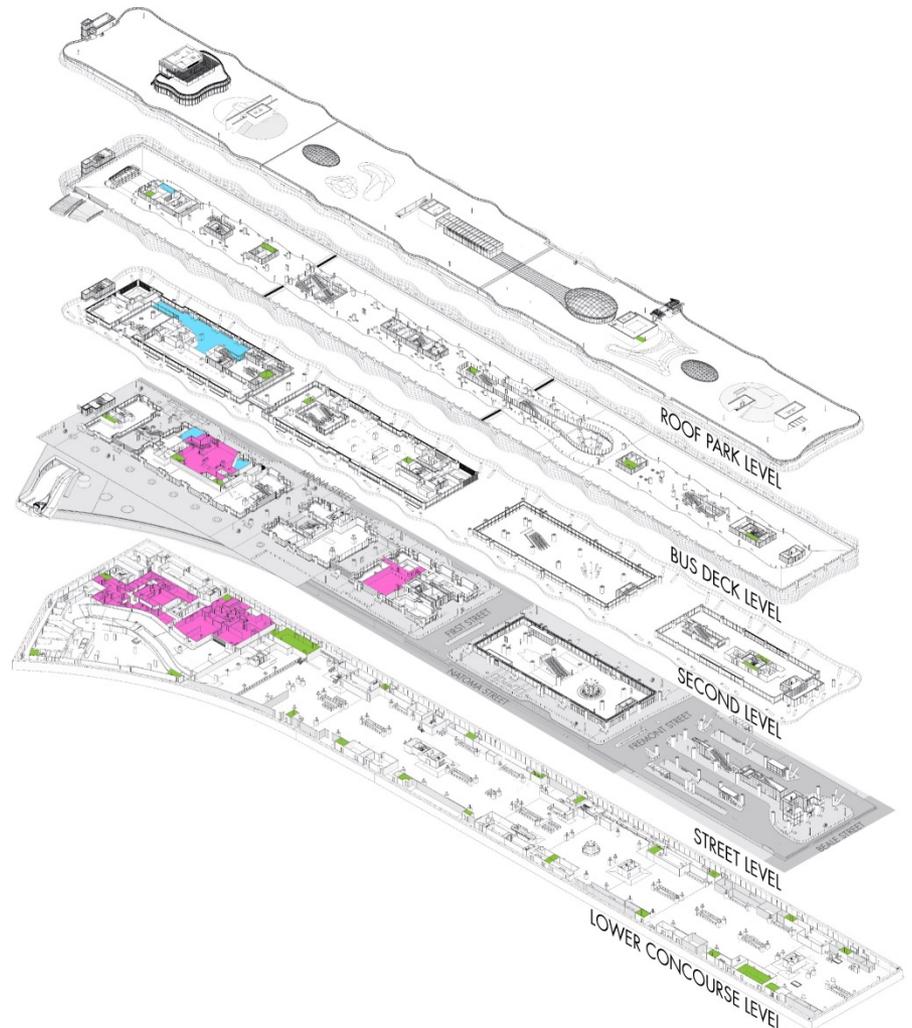



Questions?

TJPA
TRANSBAY JOINT POWERS AUTHORITY

201 Mission Street, Suite 2100 San Francisco, CA 94105 • 415.597.4620 • www.tjpa.org
