


# Update on Construction Closeout of the Salesforce Transit Center

September 10, 2020

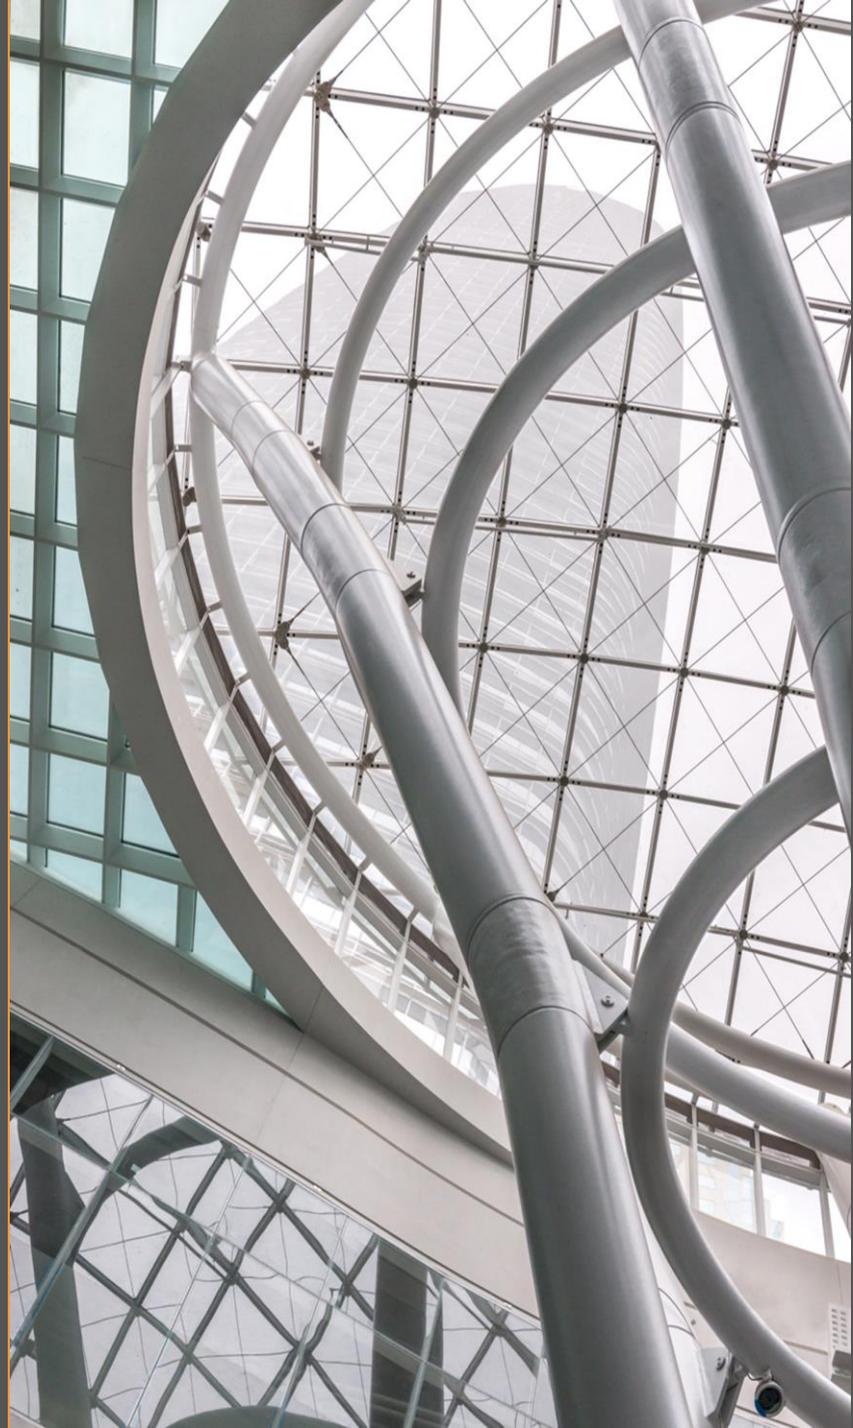


# Contract Close out Status

---

## Trade Group status:

- 1 Trade Group in the Full & Final change order process
- 11 Trade Groups proceeding to Dispute Resolution
- 37 Trade Groups are closed out

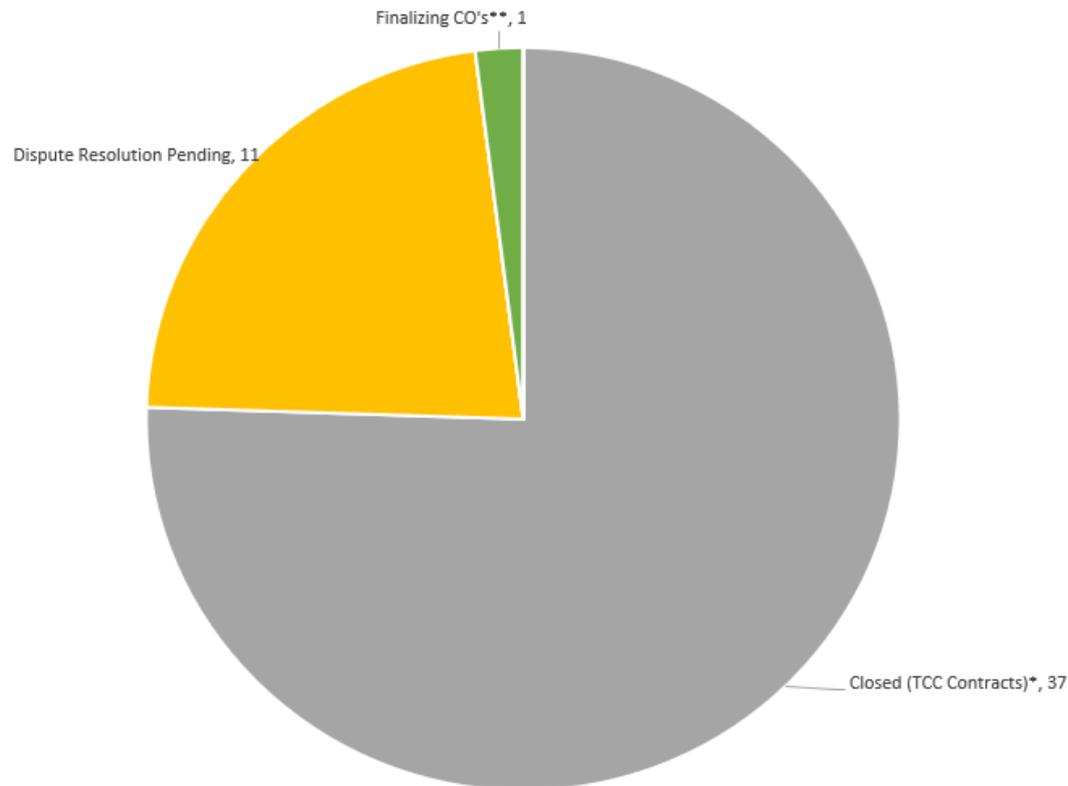

# Contingency Cost Tracking

(\$millions)

	Construction Contingency	CM/GC Contingency	Program Reserve	Total Contingency & Reserve
<b>Baseline Budget Amounts</b>	<b>\$61.8</b>	<b>\$32.5</b>	<b>\$117.0</b>	<b>\$211.3</b>
<b>Contingency Usage Through June 2020</b>	(\$43.8)	(\$27.2)	(\$69.5)	(\$140.5)
<b>Remaining Baseline Budget Amounts (at June 2020)</b>	<b>\$18.0</b>	<b>\$5.3</b>	<b>\$47.5</b>	<b>\$70.8</b>
<b>Total Draws/Adds July &amp; Aug 2020</b>	(0.4)	(0.3)	0.0	(0.7)
<b>Remaining Balances</b>	<b>\$17.6</b>	<b>\$5.0</b>	<b>\$47.5</b>	<b>\$70.1</b>

## Uses of Contingency this period

Night concrete pours in zones 2 and 3; and other miscellaneous closeout changes.

## Forecasted Contingency Use:

CM/GC: \$1.6M

Construction: \$2.0M

Program Reserve: \$0.0M

# Budget Status

(\$millions)

	Current Budget	Expended thru 06/20*	Estimate at Completion
<b>Construction</b>	<b>1,535.4</b>	<b>1,527.5</b>	<b>1,558.5</b>
<b>Construction and CM/GC Contingencies</b>	<b>23.1</b>	<b>-</b>	<b>-</b>
<b>Design and Support Contracts</b>	<b>626.3</b>	<b>621.0</b>	<b>626.3</b>
<b>Phase 1 Target</b>	<b>2,184.8</b>	<b>2,148.5</b>	<b>2,184.8</b>
<b>Tenant Improvements (Transferred to TI Capital Project)</b>	<b>-</b>	<b>-</b>	<b>-</b>
<b>301 Mission Legal</b>	<b>27.1</b>	<b>22.0</b>	<b>27.1</b>
<b>Phase 1 Target with TI and 301M Legal</b>	<b>2,211.9</b>	<b>2,170.5</b>	<b>2,211.9</b>
<b>Program Reserve</b>	<b>47.5</b>	<b>-</b>	<b>47.5</b>
<b>Total Phase 1 Program</b>	<b>2,259.4</b>	<b>2,170.5</b>	<b>2,259.4</b>
* Some expended costs are estimated			



# Thank You

**TJPA**  
TRANSBAY JOINT POWERS AUTHORITY

425 Mission Street, Suite 250 San Francisco, CA 94105 • 415.597.4620 • [www.tjpa.org](http://www.tjpa.org)
