



Second Demolition Notice to Proceed

July 15, 2010

Transbay Transit Center







DemolitionNotices to Proceed

- NTP 1 Pre-demolition work (January 4, 2010):
 - Obtain permits/approvals necessary to perform work
 - Develop and submit information necessary to perform work
- NTP 2 Demolition work (August 7, 2010):
 - Site Preparation
 - Secure Ramps/Building
 - Mobilize Equipment
 - Demolition
 - Abatement of Hazardous Materials
 - Demolish Structures and Stockpile Materials
 - Muni OCS Work



DemolitionNotice to Proceed

- Conditions for Second Notice to Proceed
 - Certification of Phase 1 Funding
 - Temporary Terminal ready for occupancy
 - Foundation package ready for advertisement
 - Buttress, Shoring and Excavation Contract to be advertised the last week of July

Transbay Transit Center


DemolitionPhasing

Phase 1 (16 days): Aug 14, 2010 – Aug 28, 2010

Phase 2 (64 days): Aug 29, 2010 – Oct 31, 2010

Phase 3 (120 days): Nov 1 2010 – Feb 28, 2010


Phase 4 (60 days): Mar 1, 2011 – Apr 29, 2011

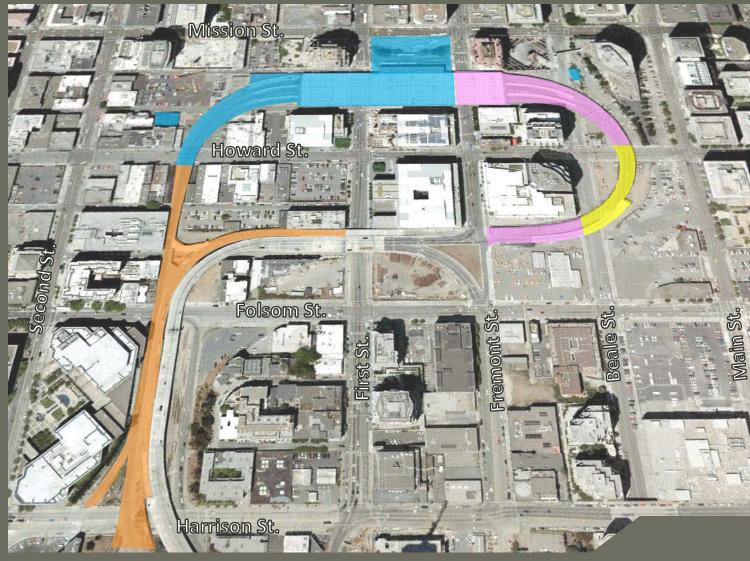

Street Closures and Bridge Demolition

Transbay Transit Center

- 1 Fri Aug 13 Mon Aug 16
- 2 Fri Aug 20 Fri Aug 27
- 3 Fri Aug 27 Sun Sept 26
- 4 Thurs Sept 30 Sun Oct 10
- 5 Thurs Oct 14 Sun Oct 24
- 6 Mon Nov 29 Wed Dec 15
- 7 Thurs Dec 16 Sun Dec. 19
- 8 Tues Jan 18 Thurs Jan 20
- 9 Thurs Feb 10 Mon Feb 14
- 10 Mon Feb 21 Wed Feb 23
- 11 Mon Mar 7- Thurs Mar 17

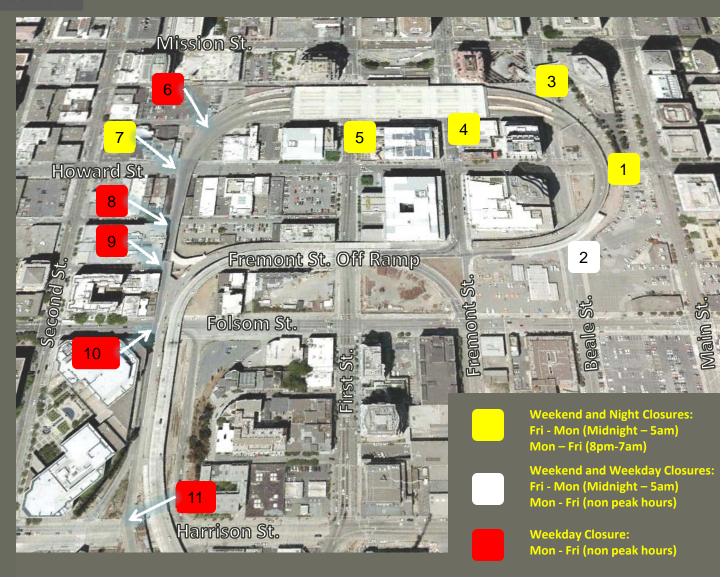

Transbay Transit Center

Nights & Weekends Traffic Impacts Demolition of Eastern Ramps

- Ramp demolition and OCS work
- Material movement to stockpile site
- Work Hours:
 Daytime (non peak)
 Nighttime (8pm 7am)
 Weekends (7am 8pm)
 (TJPA and DPW)



Impacted area



Nights & Weekends Traffic Impacts Demolition of Terminal

Transbay Transit Center

- •Ramp demolition and OCS work
- •Material movement to stockpile site
- Work Hours:
 Daytime (non peak)
 Nighttime (8pm 7am)
 Weekends (7am 8pm)
 (TJPA and DPW)



Impacted area




Transbay Transit Center

Daytime Traffic Impacts Demolition of Ramps & Terminal

- Ramp demolition and OCS work
- •Material movement to stockpile site

•Work Hours: Daytime (7am – 5pm)

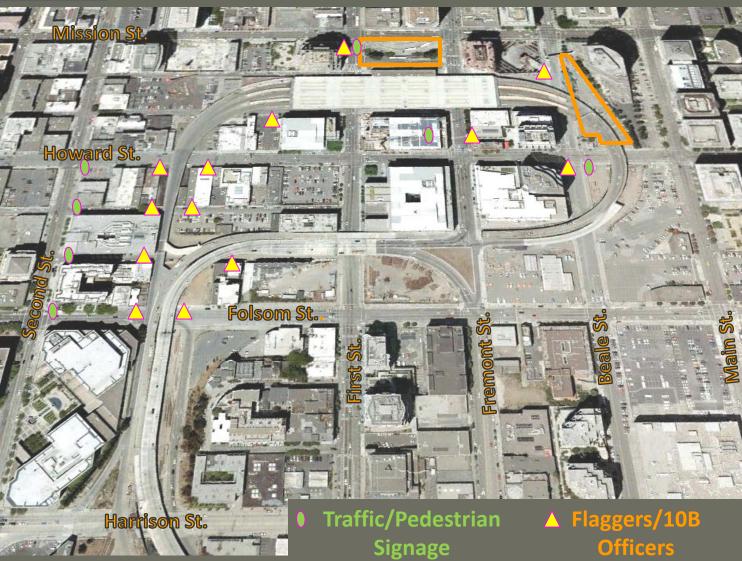

Traffic Impacts Demolition of Western Ramps

Transbay Transit Center

- Ramp demolition and OCS work
- Material movement to stockpile site
- Work Hours:
 Daytime (non peak)
 Nighttime (8pm 7am)
 Weekends (7am 8pm)
 (TJPA and DPW)



Impacted area

