



# Field Progress Update

January 11, 2011

## Transbay Transit Center

**TJPA**





Transbay Transit Center

# Field Progress Update

- Phase II and Phase III Demolition Work continued in December throughout the existing Terminal. This includes:
  - Over 27,500 craft hours without accident or incident
  - Salvage operation is now 98% complete, flagpole and steel columns remain to be delivered
  - Existing Terminal abatement work completed
  - All known ACM has been removed from site
  - Continued use of wrecking ball for central Terminal building demolition
  - Ballast removal from West approaches
- Utility Relocation Package Trade Contractors continued work, including:
  - New Water on Fremont Street, Water and Sewer work on First Street and Water work on Minna
  - Additional RUP's (4.3 and 4.4) received NTP
- 301 Mission Street Temporary Wall
  - Submittals approved, coordination with 301 Mission managers completed and contractor started January 4th



Transbay Transit Center

# Demolition Schedule

Eastern Ramps:


Aug 13, 2010 – Oct 7, 2010

Terminal Building:

Sept 20, 2010 – Feb 28, 2011

Western Ramps:

Jan 10, 2011 – Apr 29, 2011

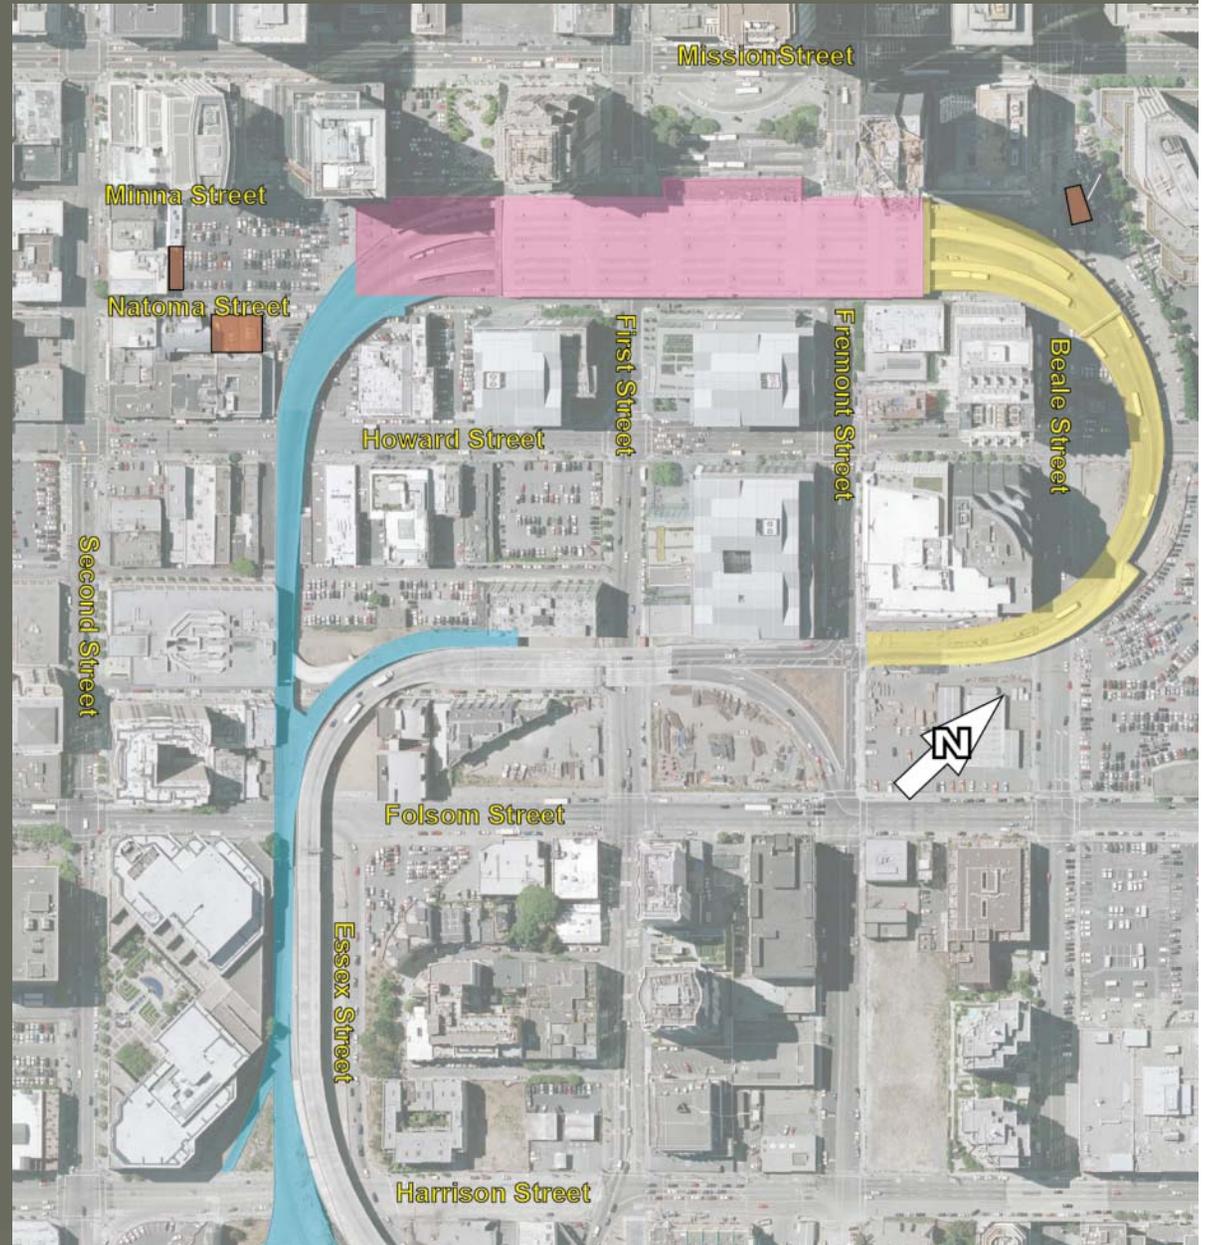



Transbay Transit Center

# Utility Relocation Trade Package Map

MISSION ST

Package TG04.2

Package TG04.6

MINNA ST

Package TG04.5.1

Package TG04.5.1

NATOMA ST

Package TG04.4

Package TG04.4

Package TG04.1

FIRST ST


FREMONT ST

BEALE ST

MAIN ST

HOWARD ST

Package TG04.3

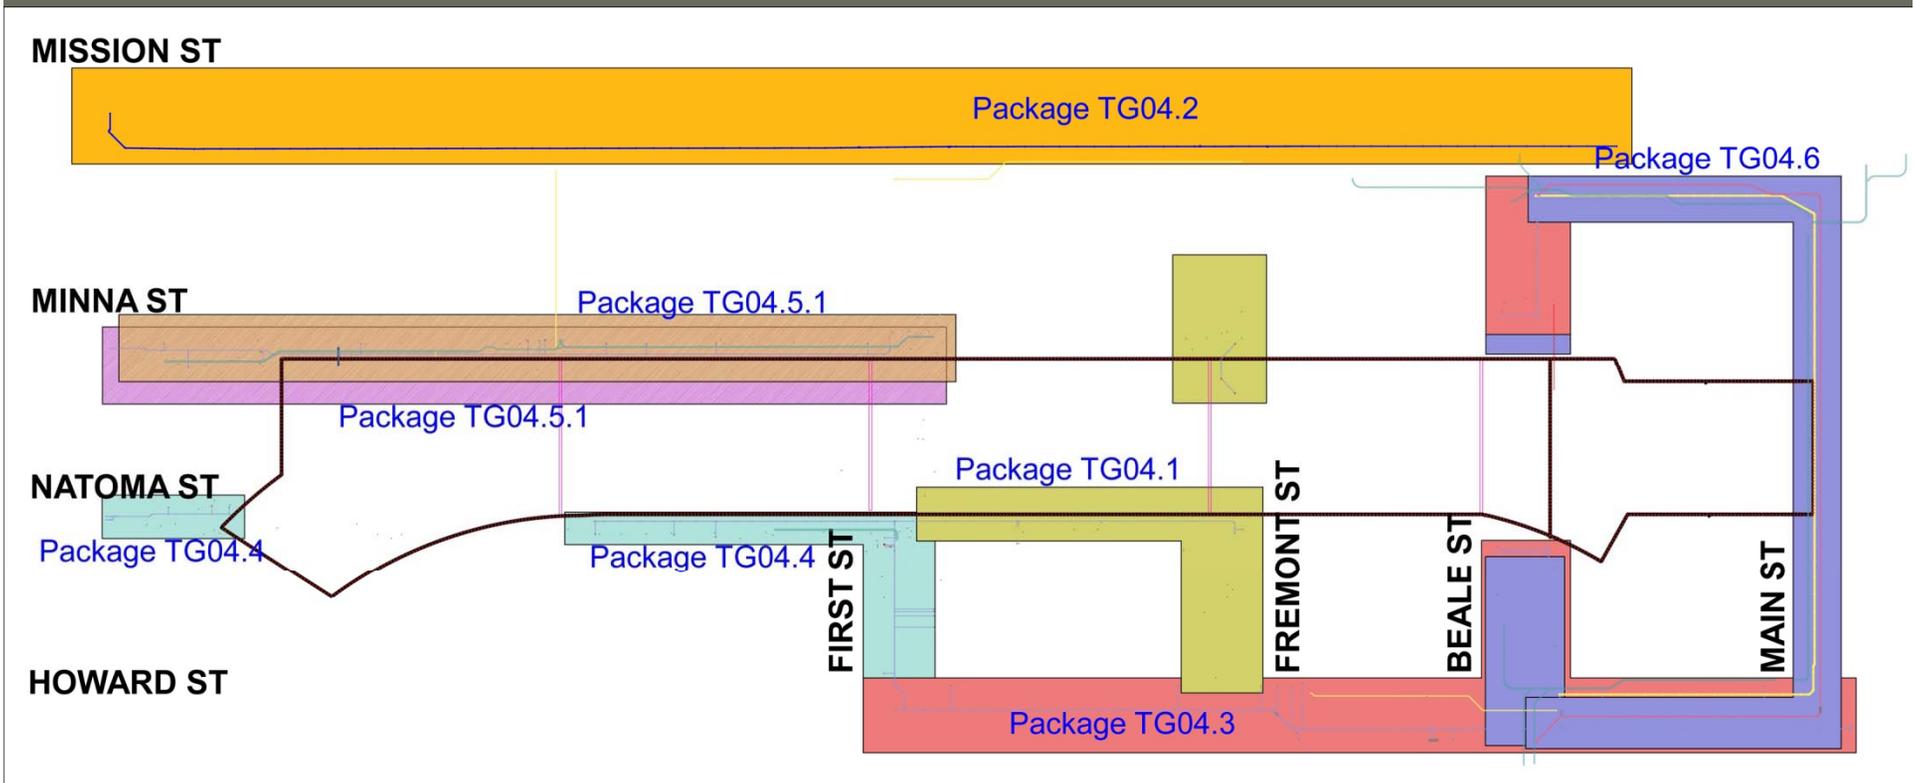



Transbay Transit Center

# East Terminal Building Demolition





Transbay Transit Center

# Central Terminal Demolition – Early December





Transbay Transit Center

# Central Terminal Demolition





Transbay Transit Center

# Removal of Ballast at West Approach





Transbay Transit Center

# Overall Demolition Status – Early January





Transbay Transit Center

# Utility Relocation on Minna





Transbay Transit Center

# New Water on Minna





Transbay Transit Center

# Water Relocation on Fremont





Transbay Transit Center


# Utility Coordination on First Street





Transbay Transit Center

# Demolition Timeline Summary

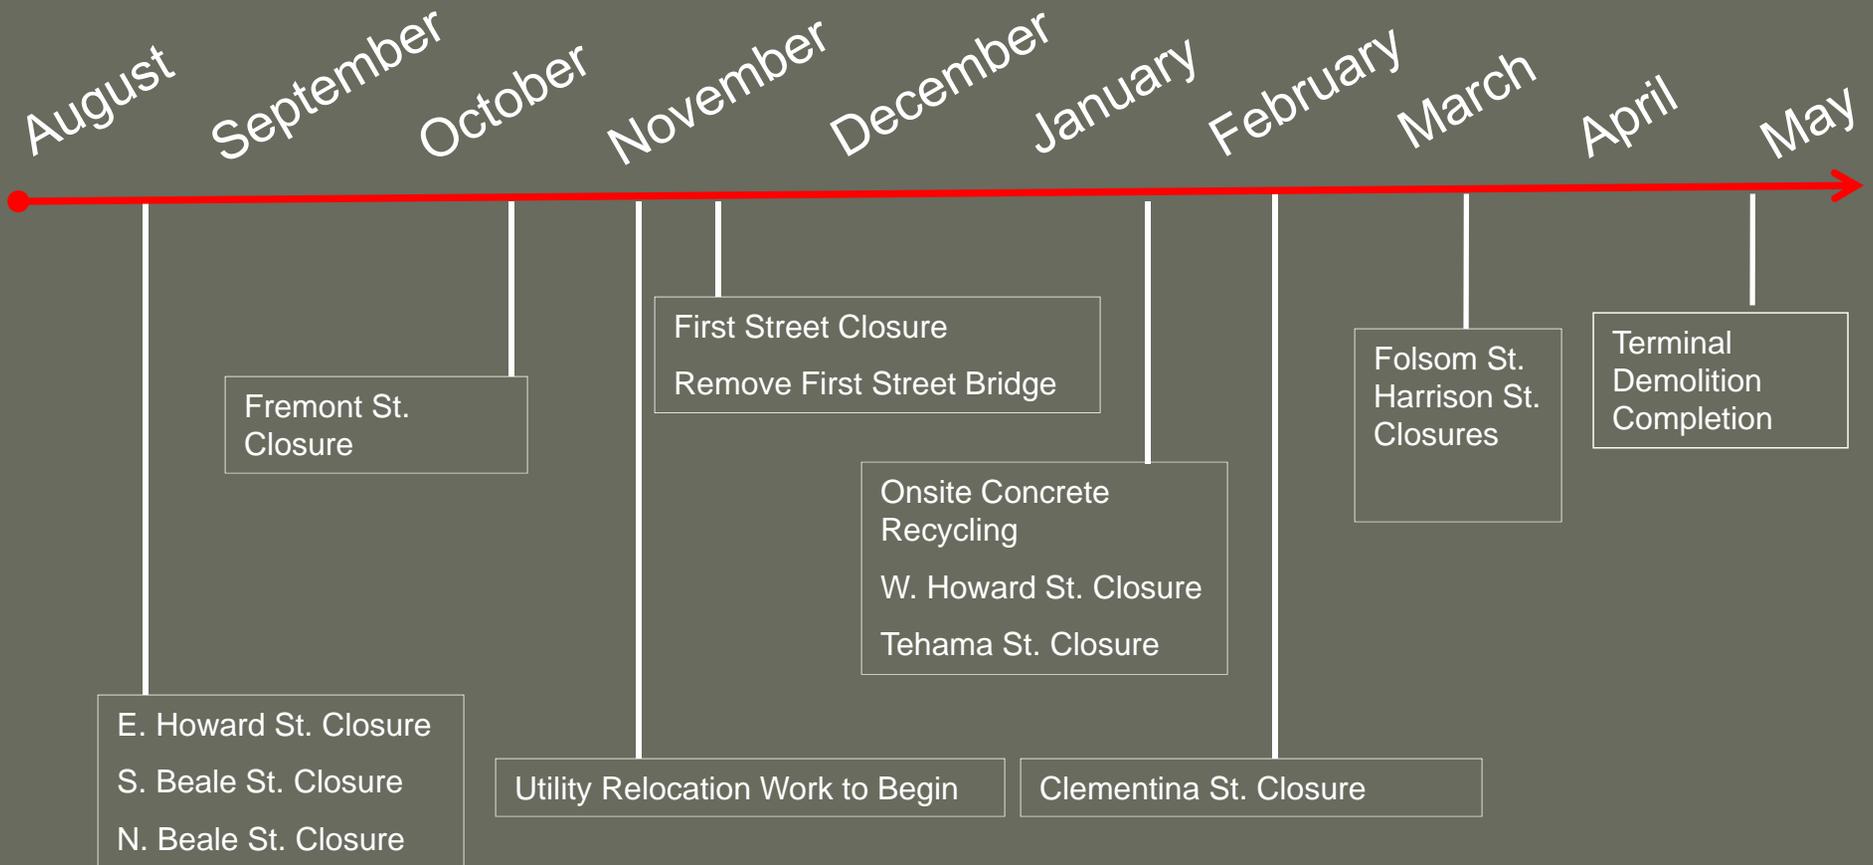



Transbay Transit Center

# Utility Relocation Timeline Summary

