## Facility Readiness Update

April 2018






#### Facility Readiness – Lincoln Tenant Improvements


- Greyhound/Amtrak
  - Ordering furniture in April
  - TJPA/Lincoln/Turner SPD & WOJV coordinating access
  - Complete mid-June at TCO
- Operational Areas
  - Mailroom equipment info received; converting info to construction docs for minor Lincoln work nearly complete
  - TJPA office bid package pending TJPA approval; Lincoln to follow
  - Estimated TJPA/Lincoln offices completion is end of July & August
- Permitting
  - TJPA/DBI delegation nearly complete



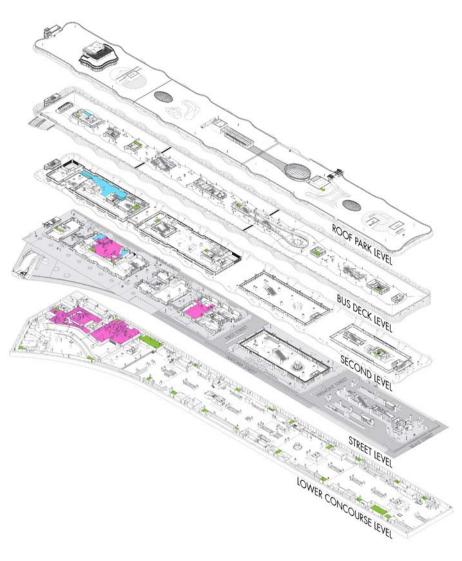

#### Facility Readiness – Lincoln Tenant Improvements


- Path of travel planning includes:
  - Attractive barricades where needed
  - Elevator programming restrictions
  - Ground level vacant storefront treatment for visual interest

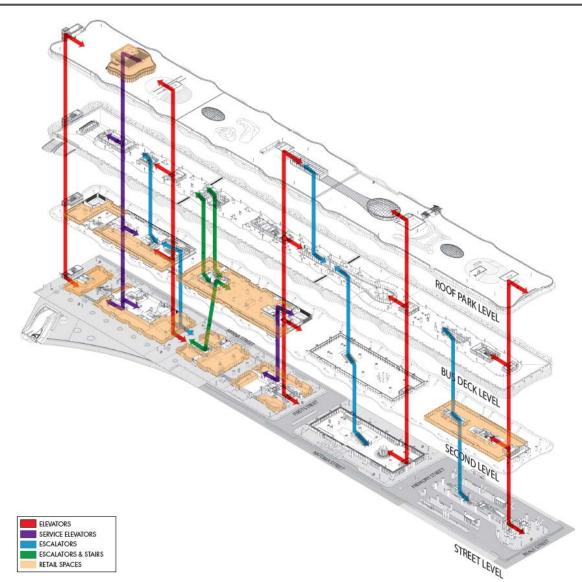



#### Facility Readiness – Lincoln Facility Maintenance

- Finalized key service contracts plus RFP on IT services released April
  2; elevator/escalator in legal review
- Branding exercise with marketing consultant underway
- Ordering equipment to start in April
- Planning operating procedures and protocols underway
- Coordinating with WOJV for commissioning observation; training to start in June
- Targeting maintenance proposal to AC Transit for Bus Storage Facility in May

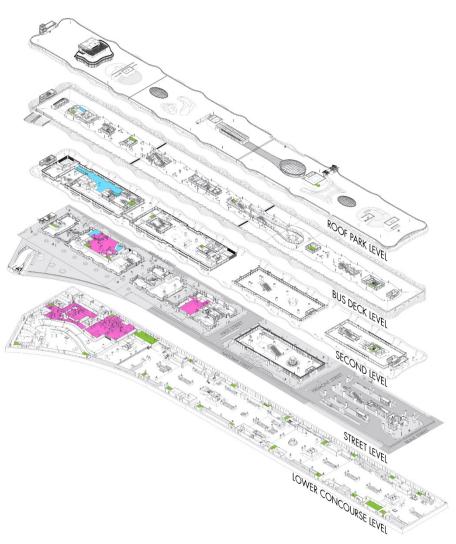



#### Facility Readiness – Lincoln Facility Maintenance


#	Contractor Name	Contracts in Place	# Bids	Low	Med	High
1	MBH Architects Inc.	Architect	4	\$170,100	\$279,000	\$320,000
2	Johnson Controls	Building management systems controls contractor	1	\$25,120	no response by others	
3	KKCS - Consulting Services	Civil engineer for emergency response to earthquake, etc.	1	\$100-198/hr	no response by others	
4	Angus Anywhere	CMMS (Computer Maintenance Management System)	2	\$1,500	\$2,046	
5	Sothern Oil Co.,	Diesel fuel services for generator & fire pump	2	\$20,698		\$40,800
6	Complete Security	Door hardware & lock contractor	3	\$69-\$148/hr	\$147-\$180/hr	incomplete
7	W.Bradley Electric	Electrical contractor	2	\$142-\$168/hr	\$75-\$177/hr	
8	Next Gen/SRM - this week	Emergency & hazardous material clean-up	4	\$65-\$140/hr	\$98-\$150/hr	2 incomplete
9	Red Hawk	Fire life safety services (alarm panel & extinguishers)	1	\$28,554	no response by others	
10	Red Hawk	Fire life safety sprinkler services contractor	1	\$108,150	no response by others	
11	Red Hawk	Fire pump testing services	1	\$2,790	no response by others	
12	Cintas	First aid kit supplier	2	\$20,798	incomplete	
13	Turner Special Projects Division	General contractor	3	3.5%/\$109K	3.5%\$209K	5% fees/incomp
14	Next Gen/SRM - this week	Hazmat cleanup contractor	4	\$65-\$140/hr	\$98-\$150/hr	2 incomplete
15	ACCO	HVAC / mechanical contractor	3	\$52,200	incomplete	\$157,084
16	Township Building Services	Janitorial	3	\$740,427	\$771,885	\$779,872
17	Maguire & Hester	Landscaping		2 years covered with installation contract		
18	Spritz	Marketing consultant	4	\$282,500	\$343,000	\$524,000
19	Myers+Engineering	MEP consultant, on-call as needed	2	\$75-\$285/hr		\$80-\$280/hr
20	Waxie	Paper & sanitary supplies	3	\$63.25/unit avg	\$284.58/unit avg	incomplete
21	Crane	Pest control	3	\$29,064/incomp	\$70,000	\$86,400
22	ACCO	Plumbing contractor	1	\$195/hr	combined bid response with Line 15	
23	Landmark Industries	Refuse & recycling stream management	2	incomplete	\$58,800	
24	Aliea Corp.	Sharps/red waste removal	1	\$31,181	no response by others	
25	Township Engineering	Stationary engineering	4	\$700,199	\$741,314	\$761,992
25	Chem-Aqua	Water treatment	3	incomplete	\$15,950	\$55,616

Note: where only one bid received; Lincoln validation that within reasonable industry pricing and quality vendor. Note: Yellow high-lighted contracts are for on-call services so, costs not incurred unless needed.



#### Facility Readiness – BRV Roof Park


- 27 solid partners; pending completing agreement template
- Completing Place of Entertainment framework for Board input May/June:
  - Policy vision
  - Event/activity limits
  - Pricing rationale and structure
  - Revenue and non-revenue generating structure

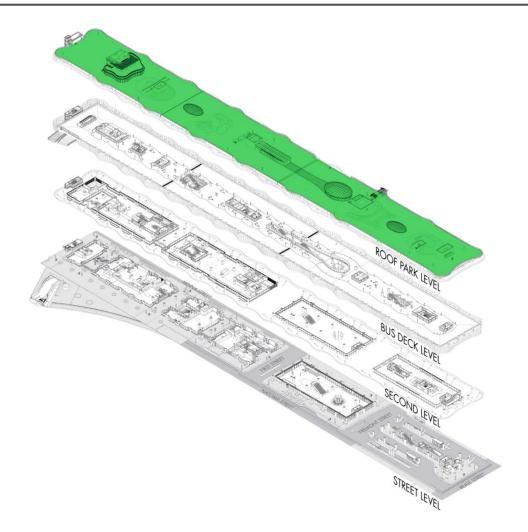



#### Facility Readiness – Pearl Digital Media


- Targeting completing SFMTA info to Pearl by April 15 for transit screen information
- Targeting completing AC Transit info to Pearl by May 1 for transit screen information
- Received 100% of transit media players. Prioritizing configuration for bus plaza operations to be ready for testing June 1 for Muni operations June 16; remainder to follow for August date
- Targeting media commitments to begin in the Fall with major brands to follow in 2019; timing due to advertisers holding back until post opening to asses activity

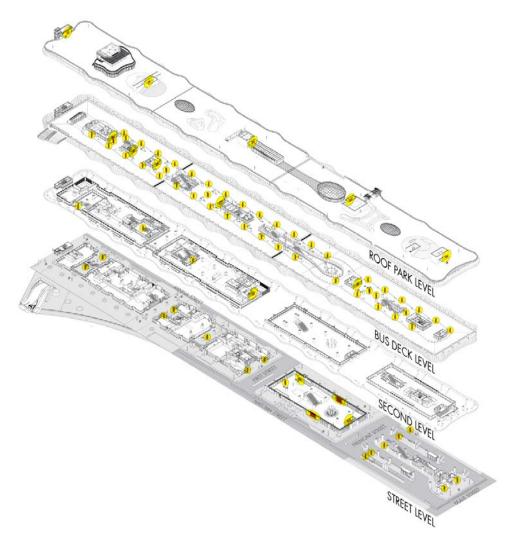



#### Facility Readiness – PRI Pop-Up Retail


- Completed comprehensive plan to include revenue projections
- Continue to market pop-up spaces with ongoing coordination with BRV, Pearl, and Colliers
- Finalizing agreements for bus plaza by June 15 and rest for August 12
- Presentation of program in May

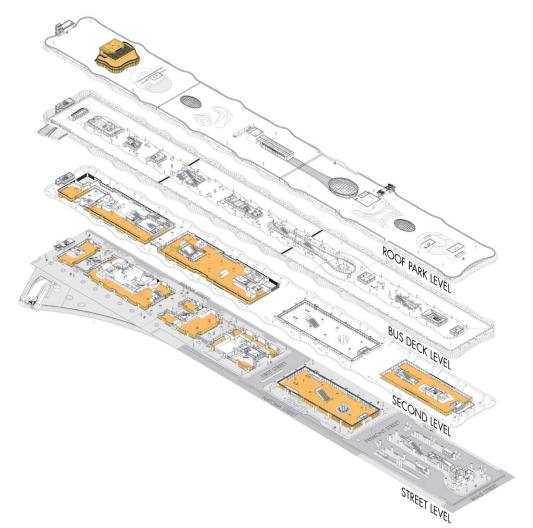



#### Facility Readiness - Transit

- Vacating temporary terminal notices to be updated in May
- SFTMA agreements for bus plaza lease and ancillary agreements nearly complete; TJPA Board in May
- Continuing to work with AC Transit to support completing license agreements
- Targeting TJPA Board in June for Amtrak who is ready to commit to 2<sup>nd</sup> floor lease with TJPA pending coming to terms with AC Transit for bus deck

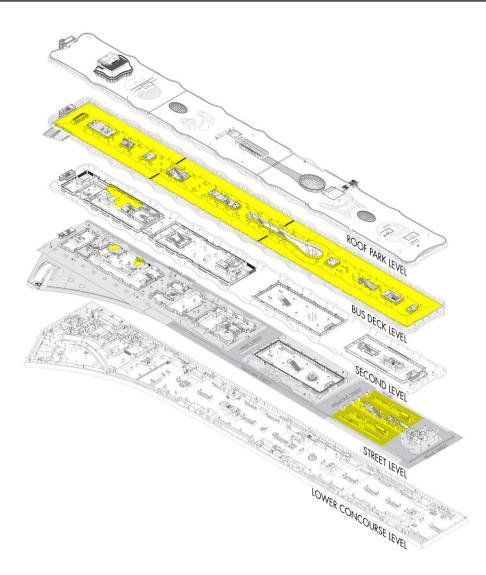





#### Facility Readiness - Security

- BOS approved legislation to include Salesforce Park in the SF Municipal Code during their first April meeting
- Standard Operating Procedures are under development & will be in place prior to start of revenue service
- On-site security training will begin June 1st
- PSIM and ECS/MNS project will be complete in June 2018, provided the security team has access to the building, with operable security systems, in due time
- Bus Plaza security will remain in place, under the Temporary Terminal contract, when it fully opens for start of revenue service




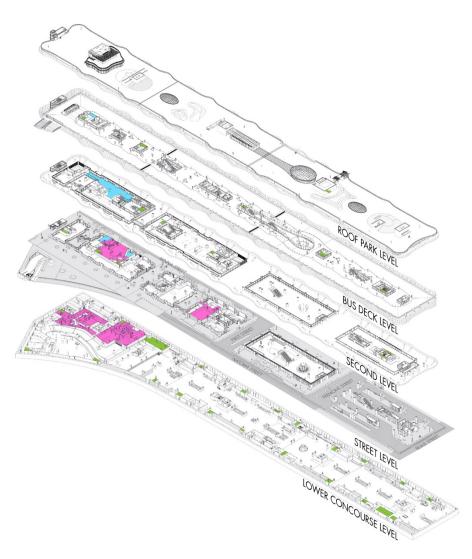

### Schedule

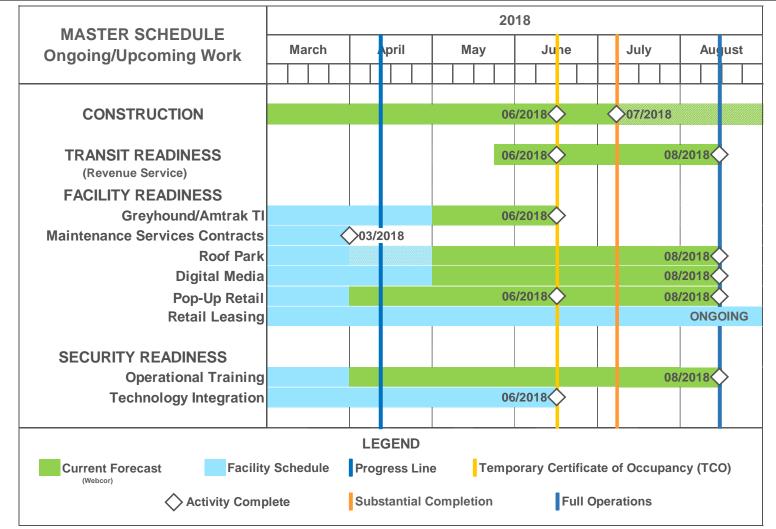



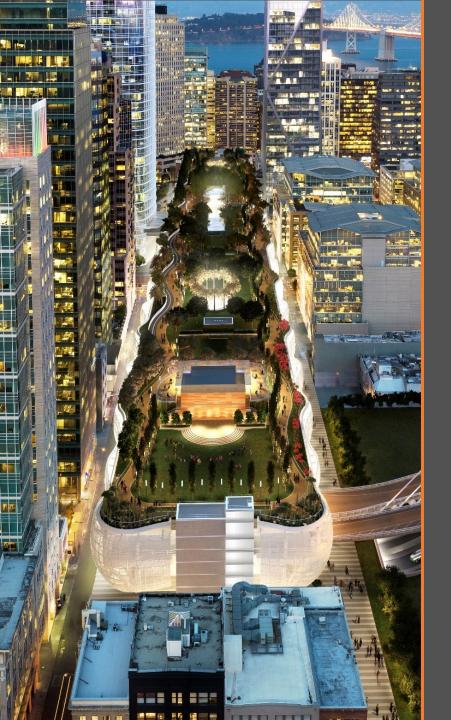

# Questions?



201 Mission Street, Suite 2100 San Francisco, CA 94105 • 415.597.4620 • www.tjpa.org
