

FINAL

1                   **The Portal Project Implementation Memorandum of Understanding**  
2  
3

---

4  
5  
6   The Portal Project Implementation Memorandum of Understanding (MOU), effective  
7   January 30, 2025, is between the Transbay Joint Powers Authority (TJPA); the Metropolitan  
8   Transportation Commission (MTC); the San Francisco County Transportation Authority  
9   (SFCTA); the Peninsula Corridor Joint Powers Board (Caltrain); the California High-Speed Rail  
10   Authority (CHSRA); and the City and County of San Francisco (CCSF) (each a “Partner” and  
11   collectively the “Partners”).  
12

13  
14   **1.    Definitions:**  
15

16   **Blueprint:** The Portal Governance Blueprint, a policy document approved by the TJPA Board in  
17   August 2023, which identifies policy recommendations for the coordination and engagement of  
18   the Partners in the implementation of the Project.  
19

20   **Change Control Board (CCB):** multi-agency body convened by the TJPA Executive Director,  
21   with representation from all six Partners, with responsibility during Phase 2 of Blueprint  
22   Implementation to review and recommend Significant Changes and Policy Changes.  
23

24   **Configuration Management Working Group (CMWG):** multi-agency body convened by the  
25   TJPA Executive Director, with representation from all six Partners, with responsibility during  
26   Phase 1 of Blueprint Implementation to review and recommend Significant Modifications to  
27   Project Configuration.  
28

29   **Executive Working Group (EWG):** multi-agency body convened and led by the TJPA  
30   Executive Director, with representation from all six Partners, with responsibility during Phase 1  
31   and Phase 2 of Blueprint Implementation to provide advice and recommendations to the TJPA  
32   Executive Director and to support the TJPA Executive Director’s reporting to The Portal  
33   Committee and TJPA Board, including review of policy items advancing to the Board level.  
34

35   **Federal Transit Administration (FTA):** the FTA is the planned grantor of federal Capital  
36   Investment Grant funds.  
37

38   **Integrated Management Team (IMT):** a senior management group, convened by the TJPA  
39   Executive Director and led by the TJPA Project Director, with representation from the Partners  
40   or from a sub-set of the Partners as mutually agreed, with responsibility during Phase 2 of  
41   Blueprint Implementation to integrate/coordinate management-level activities across the  
42   agencies, remove roadblocks and marshal resources, and provide early/ongoing visibility into  
43   Project status, issues, and risks.  
44

FINAL

45 **Integrated Program Management Team (IPMT):** a senior management group, convened by  
46 the TJPA Executive Director and led by the TJPA Project Director, with representation from all  
47 six Partners, supporting the Project during Phase 1 of Blueprint Implementation.

48  
49 **Integrated Program Delivery Team (IPDT):** the integrated team convened by the TJPA  
50 Executive Director and led by the TJPA Project Director consisting of representatives from  
51 TJPA, Caltrain, and CHSRA, their consultants and contractors, and other resources/personnel  
52 as required, with responsibility to deliver the Project.

53  
54 **IPDT Framework:** a management document describing the parameters of the IPDT.

55  
56 **Major Contracts:** The primary construction contracts through which the Project will largely be  
57 delivered, which are the Civil-Tunnel Progressive Design-Build (PDB/40-CT), Track and  
58 Systems Construction Manager-General Contractor (CMGC), Salesforce Transit Center Station  
59 Fit-Out CMGC, and Fourth and King Yard (4KY) Package B as this list may be amended by  
60 mutual agreement of the Partners.

61  
62 **Minor Change:** A Project Change that does not conflict with the Policy Baseline and is less  
63 than a threshold defined in the CCB Charter.

64  
65 **Partners:** the six agencies party to this MOU: the Transbay Joint Powers Authority (TJPA); the  
66 Metropolitan Transportation Commission (MTC); the San Francisco County Transportation  
67 Authority (SFCTA); the Peninsula Corridor Joint Powers Board (Caltrain); the California High-  
68 Speed Rail Authority (CHSRA); and the City and County of San Francisco (CCSF). Collectively  
69 the Partners and each individually a Partner.

70  
71 **Peninsula Rail Program MOU:** The San Francisco Peninsula Rail Program Memorandum of  
72 Understanding, executed among the Partners in 2020 and having expired on May 10, 2024.

73  
74 **Phase 1 of Blueprint Implementation:** The first period governed by this MOU, from date of  
75 completion of this MOU's execution by all six Partners until the start of Phase 2 of Blueprint  
76 Implementation as defined herein, during which time The Portal Board Committee will be  
77 established. Also, during this time, the TJPA Executive Director has confirmed, and the Partners  
78 have concurred, that regular meetings of EWG, CMWG, IPMT, and IPDT will be held, as  
79 described in Section 7 of this MOU.

80  
81 **Phase 2 of Blueprint Implementation:** The final period governed by this MOU, to take effect  
82 no later than the Start of Project Delivery, as defined herein, and continuing through the term of  
83 this MOU. During this time, the TJPA Executive Director has confirmed, and the Partners have  
84 concurred, that regular meetings of EWG, CCB, IMT, and IPDT will be held, as described in  
85 Section 7 of this MOU.

86  
87 **Policy Change:** A Project Change that significantly alters or threatens the planned outcomes of  
88 the Project, or otherwise exceeds a threshold defined in the CCB Charter for a Policy Change,  
89 including all changes that are materially inconsistent with the Policy Baseline.

90

FINAL

91 **Policy Baseline:** a collection of formal documents, to be brought forward for consideration by  
92 the TJPA Board, that will collectively describe the Project's scope, schedule, budget, funding  
93 plan, and risk approach.

94  
95 **Project:** The Portal, also known as the Downtown Rail Extension, as described in Section 5 of  
96 this MOU.

97  
98 **Project Change:** A modification to the Project's configuration, schedule, budget, and/or  
99 contracts (including changes to contract scope, schedule, and/or cost).

100  
101 **Project Configuration:** The combined physical, functional, and operational characteristics of  
102 structures, systems, and components of the Project.

103  
104 **Revenue Service:** Regular rail operations on the Project that serve fare-paying passengers.

105  
106 **Significant Change:** A Project Change that does not conflict with the Policy Baseline and that  
107 exceeds a threshold defined in the CCB Charter.

108  
109 **Significant Modification to Project Configuration:** A modification to Project Configuration  
110 with a material impact on the planned outcomes of the Project.

111  
112 **Start of Project Delivery:** The date of the first award of any construction contract for the  
113 Project, specifically the earliest date of either: the award of the pre-construction phase of the  
114 Civil-Tunnel Progressive Design-Build (PDB/40-CT) contract; or the award of the first enabling  
115 construction contract package, including packages for the Fourth and King Railyard.

116  
117 **Status Report:** a report prepared monthly by the Integrated Program Delivery Team.

118  
119 **Stage Gates:** a sequence of formal review points during the Project to assess the Project's  
120 readiness to advance and to make recommendations to the TJPA Board.

121  
122 **Summary Work Program:** A document describing the Project's activities and Partner roles and  
123 responsibilities in these activities over at least the coming two years, to be updated annually and  
124 presented to the TJPA Board.

125  
126 **The Portal Committee:** a standing committee of the TJPA Board, providing transparent and  
127 dedicated venue for review and recommendation to the TJPA Board of policy matters to be  
128 established during Phase 1 of Blueprint Implementation and to continue during Phase 2 of  
129 Blueprint Implementation.

130  
131

132 **2. Purpose:**

133  
134 The Partners recognize that The Portal is a critical rail link in the Bay Area, Northern California  
135 mega-region, and statewide transportation system and that it will be most efficiently and

FINAL

136 effectively delivered through a multi-agency partnership among local, regional, and state  
 137 stakeholder agencies with expertise in developing, funding, and implementing major  
 138 infrastructure projects.

139  
 140 This MOU describes the multi-agency coordination, administrative organizational structure, and  
 141 processes that will support the efforts of the TJPA in the delivery of The Project. This MOU is  
 142 intended to be consistent with the policy recommendations of The Portal Governance Blueprint,  
 143 which is attached to this MOU and incorporated by reference herein. In the event of  
 144 inconsistency between the MOU and the Blueprint, the MOU shall take precedence.

145  
 146 This MOU describes the currently contemplated primary roles and responsibilities of each of the  
 147 Partners. This MOU does not establish funding contributions or payment between the parties.

148  
 149  
 150 **3. Partner Agency Primary Roles and Responsibilities:**

151  
 152 The Partners recognize that – and nothing in this MOU is intended to imply otherwise – state  
 153 law and the TJPA’s 2001 Joint Powers Agreement (as amended) provide that the TJPA has  
 154 primary jurisdiction over and will implement The Portal that will connect the Salesforce Transit  
 155 Center to the regional rail system and to the statewide high-speed rail system.

156  
 157 The Partners also recognize that each Partner has roles and responsibilities associated with the  
 158 development and delivery of the Project. The Partners also recognize that each Partner bears  
 159 certain risks associated with the Project and that the cooperation and engagement of all  
 160 Partners is necessary to effectively manage Project risks. In addition to the Partners’  
 161 participation in the management and organizational processes described in this MOU, each  
 162 Partner’s currently contemplated primary roles and responsibilities associated with delivery of  
 163 the Project are summarized as follows:

164  
 165 **TJPA** is the lead agency and FTA grantee. TJPA is responsible for: managing the  
 166 development, environmental clearance, design, procurement, construction, and  
 167 commissioning of the Project; leading integration of all elements of the Project; ensuring  
 168 the Project is compliant with FTA requirements; and managing and administering the  
 169 governance, management, Partner engagement, and organizational processes and  
 170 structures required to deliver the Project. TJPA will hold the Project’s construction  
 171 contracts, with the exception of any contract separately agreed by TJPA and any other  
 172 Partner to be held by that Partner. TJPA is the FTA grantee and will lead and manage  
 173 the Project’s relationship with FTA.

174  
 175 **Caltrain** is expected to be the initial rail service operator providing regional rail service  
 176 for The Portal. Caltrain owns and operates the corridor leading to The Portal.

177  
 178 **CHSRA** is expected to be a subsequent rail service operator providing statewide high-  
 179 speed rail service for The Portal.

FINAL

180  
181  
182  
183  
184  
185  
186  
187  
188  
189  
190  
191  
192  
193  
194  
195  
196  
197  
198  
199  
200  
201  
202  
203  
204  
205  
206  
207  
208  
209  
210  
211  
212  
213  
214  
215  
216  
217  
218  
219  
220  
221  
222  
223

**Both Caltrain and CHSRA will participate in a technical working group established as part of the Integrated Program Delivery Team (IPDT) to address and finalize technical requirements of infrastructure including tunnel, systems performance, safety and security in order to meet or exceed federal and state laws and regulations for both Caltrain and CHSRA operations and protect public health and safety. Responsibilities shall be as described in the IPDT Framework agreed upon between TJPA and the operators. The escalation path described in the IPDT Framework will be used to resolve any disagreement between Caltrain and CHSRA.**

**CCSF is the combined City and County host jurisdiction, planner and operator of CCSF infrastructure and services, a transportation planning agency, a transit agency, and a local funding entity. CCSF is responsible for: oversight and permitting related to streets, the Muni transit system, public realm, CCSF utilities, and other existing and future CCSF infrastructure and services; requiring that Project impacts to CCSF infrastructure and services are adequately mitigated; oversight and approval of CCSF infrastructure to be built or modified by the Project; coordinating input from CCSF departments, agencies, boards, and commissions; and participating in the planning, design, and implementation of the Project as requested or required by law.**

**SFCTA is the congestion management agency for San Francisco under state law and serves as sub-regional transportation planning agency and administrator of multiple local transportation funding sources. SFCTA is responsible for: conducting project management oversight of Project development and Project delivery, on behalf of the SFCTA Board and as a complement to oversight conducted by FTA and the FTA Project Management Oversight Consultant; serving as co-lead agency (with TJPA) for the Project’s funding strategy and supporting funding advocacy; serving as lead agency for the preparation of ridership forecasts, working in collaboration with TJPA and the other Partners; supporting planning and funding coordination among local, regional, state, and federal agencies; and participating in the planning, design, and other activities of the Project as requested or required by law.**

**MTC is the regional transportation planning, financing, and coordinating agency. MTC is a direct investor through regional bridge tolls and is the responsible agency for prioritizing regional projects for major sources of funding. MTC is responsible for: providing a regional perspective in risk management and change management to ensure the responsible use of funds, consistency with policy commitments, and delivery of the Project as a sustainable and seamless component of the wider regional transportation network; and participating in the planning, design, and other activities of the Project as requested or required by law.**

**The Partners’ specific roles and responsibilities will be periodically refined and elaborated in the Summary Work Program, as described in Section 13 of this MOU.**

FINAL

224  
225  
226  
227  
228  
229  
230  
231  
232  
233  
234  
235  
236  
237  
238  
239  
240  
241  
242  
243  
244  
245  
246  
247  
248  
249  
250  
251  
252  
253  
254  
255  
256  
257  
258  
259  
260  
261  
262  
263  
264  
265  
266  
267

**4. Term and Procedure for Amendment:**

4.1 The term of this MOU shall be through the date of completion of the latest of the following milestones: substantial completion of the Major Contracts (as defined in those contracts); and the completion of a project evaluation report, to be presented to the TJPA Board within 12 months after the start of Revenue Service.

4.2 The Partners may amend, conclude or extend this MOU by mutual agreement; such agreement shall be evidenced in writing. Notwithstanding the foregoing, the TJPA may terminate this MOU in its discretion by action of the TJPA Board; prior to any such proposed termination, the TJPA shall meet and confer with the other Partners in a good faith effort to resolve any concerns and avoid the need for termination. Any other Partner may withdraw from this MOU in its discretion, following a meet-and-confer with the other Partners in a good faith effort to resolve any concerns and avoid the need for withdrawal. In the event that a Partner withdraws from this MOU, the remaining Partners will continue to cooperate as described herein.

**5. Project Description:**

The Portal, also known as the Downtown Rail Extension or DTX, will connect Caltrain's regional rail system and CHSRA's future statewide system to the Salesforce Transit Center in downtown San Francisco. The Project is an essential part of a long-term strategy to create seamless connections among local, regional, and statewide transportation systems and connect rail to important locations throughout the Northern California mega-region. The rail alignment will be constructed principally below grade to provide a critical link for Peninsula commuters and travelers on the state's future high-speed rail system.

**6. Blueprint Implementation:**

The Partners recognize that the Project will proceed into procurement and construction over time, and, as such, the Partners agree to a phased approach for engagement in the Project consistent with the Blueprint. Under this approach, the Blueprint's policy recommendations will proceed in two phases, as follows:

**Phase 1 of Blueprint Implementation (Transition Phase):** an initial transition period, whereby the Blueprint's policy recommendations will be partially achieved. The term of Phase 1 will be from the date of execution of this MOU by all Partners until the date of start of Phase 2 of Blueprint Implementation, as described herein. During Phase 1, the TJPA Board will establish The Portal Committee. During this time, the TJPA Executive Director has confirmed, and the Partners have concurred, that regular meetings of EWG, CMWG, IPMT, and IPDT will be held, in the manner described in Section 7 of this MOU.

FINAL

268  
269  
270  
271  
272  
273  
274  
275  
276  
277  
278  
279  
280  
281  
282  
283  
284  
285  
286  
287  
288  
289  
290  
291  
292  
293  
294  
295  
296  
297  
298  
299  
300  
301  
302  
303  
304  
305  
306  
307  
308  
309

**Phase 2 of Blueprint Implementation (Blueprint Fully Implemented):** all policy recommendations codified in the Blueprint will be in place no later than the Start of Project Delivery, as defined herein. Phase 2 will be through the term of this MOU, as defined herein. The Portal Committee will be continued during Phase 2. During this time, the TJPA Executive Director has confirmed, and the Partners have concurred, that regular meetings of EWG, CCB, IMT, and IPDT will be held, in the manner described in Section 7 of this MOU.

**7. Multi-Agency Coordination and Engagement:**

The processes for multi-agency coordination and engagement amongst the Partners are described by this MOU as summarized below.

**7.1 The Portal Committee of the TJPA Board**

The TJPA Board holds decision authority on all matters related to the Project, including policy matters. The TJPA Board shall establish The Portal Committee, as a standing committee of the TJPA Board. The TJPA Board shall establish The Portal Committee prior to the start of Phase 2 of Blueprint Implementation.

The TJPA Board will appoint the membership of The Portal Committee. The Portal Committee shall consist of three voting members and shall be appointed by the TJPA Board according to its bylaws. The TJPA Board shall invite MTC to designate a non-voting representative to The Portal Committee.

The Portal Committee will provide a transparent and dedicated venue for review and recommendation of policy matters and decisions pertaining to the Project. The Committee will also conduct oversight of Project management and Project performance. The Committee shall report regularly to the TJPA Board and shall make recommendations for consideration by the full TJPA Board. The Committee shall convene at least quarterly and may convene more frequently as the Project may require.

**7.2 Executive Working Group**

The TJPA Executive Director, of their own authority, has convened an Executive Working Group (EWG) for the Project, to provide the Executive Director with advice and recommendations about the delivery of the Project. The TJPA Executive Director confirmed, and the Partners concurred, that the EWG will convene on an ongoing basis throughout Phase 1 and Phase 2 of Blueprint Implementation.

## FINAL

310 The TJPA Executive Director confirmed, and the Partners concurred, that the EWG consists of  
311 the chief executives (or their designee) of TJPA, MTC, SFCTA, Caltrain, CHSRA, and CCSF  
312 (for CCSF, the EWG member will be the Mayor's designee).

313  
314 The TJPA Executive Director requested, and the Partners concurred, that the EWG support the  
315 Executive Director's executive-level management of the Project, including consideration of the  
316 Partners' best practices and lessons learned. The Executive Director requested, and the  
317 Partners concurred, that the EWG provide policy review support to the TJPA Executive Director  
318 and support the TJPA Executive Director's reporting to The Portal Committee and TJPA Board,  
319 including review of policy items advancing to the Board level. The Executive Director requested,  
320 and the Partners concurred, that the EWG also receive and provide input on issues escalated,  
321 through the TJPA Executive Director, by the TJPA Project Director, the Integrated Program  
322 Management Team, and the Integrated Management Team. The TJPA Executive Director  
323 requested, and the Partners concurred, that the EWG provide the Executive Director with  
324 recommendations for their consideration.

### 325 326 7.3 Integrated Program Management Team

327  
328 The TJPA Executive Director, of their own authority, has convened the Integrated Program  
329 Management Team (IPMT) to support development and delivery of the Project during Phase 1  
330 of Blueprint Implementation. The TJPA Executive Director confirmed, and the Partners  
331 concurred, that the IPMT will regularly meet until such time as the IMT and the CCB begin  
332 regularly meeting. The TJPA Executive Director confirmed, and the Partners concurred, that the  
333 TJPA Project Director will continue to lead the IPMT.

334  
335 The TJPA Executive Director confirmed, and the Partners concurred, that the IPMT will continue  
336 to consist of representatives from each of the Partners with relevant experience in large  
337 complex projects, as designated by their corresponding EWG member. The TJPA Executive  
338 Director requested, and the Partners concurred, that each EWG member designate a lead IPMT  
339 member and an alternate IPMT member for the respective Partner, and that the IPMT will  
340 continue to be supported by additional relevant qualified personnel from the Partners and their  
341 consultants.

342  
343 The TJPA Executive Director confirmed, and the Partners concurred, that, during Phase 1 of  
344 Blueprint Implementation, the IPMT will: provide technical review support, input, and  
345 coordination to the Project's work program of project development, procurement preparation,  
346 procurement, and other activities; recommend Policy Baseline documents and Stage Gate  
347 milestones; review Status Reports; and provide input on the development of the Summary Work  
348 Program. The TJPA Executive Director confirmed, and the Partners concurred, that the IPMT  
349 will review items advancing to the EWG through the TJPA Executive Director, and IPMT  
350 members will provide staff support to respective EWG members.

351  
352 The TJPA Executive Director confirmed, and the Partners concurred, that they will continue to  
353 convene the IPMT, that the TJPA Project Director will continue to lead the IPMT, and that TJPA

## FINAL

354 will be responsible for managing IPMT proceedings, including agenda management, advance  
355 provision of materials, and documentation of meetings.

356

357 **7.4 Configuration Management Working Group**

358

359 The TJPA Executive Director, of their own authority, has convened the Configuration  
360 Management Working Group (CMWG). The TJPA Executive Director confirmed, and the  
361 Partners concurred, that the CMWG will meet when required during Phase 1 of Blueprint  
362 Implementation, until such time as the Integrated Management Team and the Change Control  
363 Board begin meeting regularly.

364

365 The TJPA Executive Director confirmed, and the Partners concurred, that the CMWG will  
366 continue to consist of each Partner's lead representative on IPMT.

367

368 The TJPA Executive Director confirmed, and the Partners concurred, that the CMWG will  
369 continue to be responsible for reviewing proposed Significant Modifications to Project  
370 Configuration and for making recommendations regarding the adoption of such changes to the  
371 TJPA Executive Director for discussion at the EWG and/or The Portal Committee. The TJPA  
372 Executive Director confirmed, and the Partners concurred, that the TJPA Project Director will  
373 continue to be responsible for managing CMWG process and proceedings, including agenda  
374 management, advance provision of materials, documentation of meetings, and preparation of  
375 additional analysis to support decision-making.

376

377 **7.5 Change Control Board**

378

379 The TJPA Executive Director, of their own authority, has convened a Change Control Board  
380 (CCB) for the Project. The TJPA Executive Director confirmed, and the Partners concurred, that  
381 the CCB will meet regularly starting during Phase 2 of Blueprint Implementation, as defined  
382 herein.

383

384 The TJPA Executive Director confirmed, and the Partners concurred, that the CCB includes  
385 representation from each of the Partners.

386

387 The TJPA Executive Director confirmed, and the Partners concurred, that the CCB will: consider  
388 and recommend Policy Changes and Significant Changes, as described in Section 10 of this  
389 MOU; and regularly review Project Change reports documenting Project Changes approved  
390 beneath thresholds defined in the CCB Charter for Significant Changes. The TJPA Executive  
391 Director confirmed, and the Partners concurred, that the CCB will also: support risk  
392 management activities; support identification of policy matters requiring review and decision-  
393 making; and perform other duties to the extent specified in the CCB Charter.

394

395 During Phase 1 of Blueprint Implementation, the TJPA Executive Director confirmed, and the  
396 Partners concurred, that the IPMT will prepare a recommended CCB Charter and that the CCB  
397 Charter will codify: the CCB's standard meeting frequency and standing agenda structure;

## FINAL

398 approach to term and rotation of the CCB Chair and Vice Chair; procedures for CCB review and  
399 recommendation of Significant Changes and Policy Changes; CCB voting composition; detailed  
400 definition of Minor Changes, Significant Changes, and Policy Changes; and respective  
401 thresholds for these types of Project Change types. The TJPA Executive Director confirmed,  
402 and the Partners concurred, that: the IPMT will recommend the CCB Charter; the TJPA  
403 Executive Director will review the recommended CCB Charter with the EWG; and the final CCB  
404 Charter will be brought forward for approval by the Partners at an executive staff level. The  
405 Integrated Program Delivery Team shall prepare and/or update relevant project management  
406 plans and procedures to be consistent with the CCB Charter.

407

#### 408 7.6 Integrated Management Team

409

410 The TJPA Executive Director, of their own authority, has convened an Integrated Management  
411 Team (IMT) for the Project. The TJPA Executive Director confirmed, and the Partners  
412 concurred, that the IMT will be led by the TJPA Project Director and that the IMT will meet  
413 regularly during Phase 2 of Blueprint Implementation, concurrent with the sunset of the  
414 IPMT and the start of regular meetings of the CCB.

415

416 The TJPA Executive Director confirmed, and the Partners concurred, that the IMT will provide  
417 advice to the TJPA Project Director and support the TJPA Project Director in the management  
418 of the Project. The TJPA Executive Director confirmed, and the Partners concurred, that the IMT  
419 will: integrate and coordinate project activities and commitments across IMT Partners; solve  
420 problems, remove roadblocks, and marshal resources; align direction to the Integrated Project  
421 Delivery Team; support risk management; and provide input to Project reporting.

422

423 The TJPA Executive Director confirmed, and the Partners concurred, that the IMT will be led by  
424 the TJPA Project Director and the IMT will include senior management representation from  
425 those Partners with the basis and capacity for participation.

426

#### 427 7.7 Integrated Program Delivery Team

428

429 The TJPA Executive Director, of their own authority, has convened an Integrated Program  
430 Delivery Team (IPDT) for the Project, consisting of representatives from TJPA, Caltrain, and  
431 CHSRA, their consultants and contractors, and other resources/personnel as required. The  
432 TJPA Executive Director confirmed, and the Partners concurred, that the IPDT will meet  
433 regularly during Phase 1 and Phase 2 of Blueprint Implementation.

434

435 The TJPA Executive Director confirmed, and the Partners concurred, that the IPDT will be the  
436 primary staff-level body with the responsibility to deliver the Project so that it can be  
437 implemented within the approved scope, budget, and schedule. The TJPA Executive Director  
438 confirmed, and the Partners concurred, that the IPDT will include team members that provide  
439 day-to-day management and delivery of the Project. The TJPA Executive Director confirmed,  
440 and the Partners concurred, that the IPDT will be comprised of dedicated staff residing in a co-  
441 located office with the support of remote teams and specialty technical experts and that each

FINAL

442 party's IPDT team members will be directly supported by their own Project organizational  
443 structures.

444

445 The TJPA Executive Director confirmed, and the Partners concurred, that the IPDT will be led  
446 by the TJPA Project Director. The TJPA Executive Director confirmed, and the Partners  
447 concurred, that the TJPA Project Director and the operators and their representatives will work  
448 cooperatively to resolve open issues regarding the Project and will be responsible for informing  
449 executive management at their respective agency of critical issues.

450

451

452 **8. Policy Baseline:**

453

454 The Partners recognize the need to structure and focus policy-level decision-making for the  
455 Project and to delegate management-level decision-making. The Partners expect that the TJPA  
456 Board will establish a Policy Baseline for the Project, with subsequent changes to the Policy  
457 Baseline controlled by the TJPA Board.

458

459 The Policy Baseline will describe the Project's scope, schedule, budget, funding plan, and risk  
460 approach. From time to time, the IPDT may prepare more detailed Baseline documents, which  
461 will be consistent with the Policy Baseline. The Policy Baseline shall consist of five documents,  
462 as follows: Project Definition; Schedule; Budget; Funding Plan; and a Policy Baseline Risk  
463 Document. Section 3 of The Portal Governance Blueprint, which is provided as Attachment #1  
464 to this MOU, summarizes the anticipated basis and anticipated content of the Policy Baseline  
465 documents.

466

467 The Policy Baseline documents shall be presented to the TJPA Board for its consideration. The  
468 Partners expect that the TJPA Board will adopt first versions of all five Policy Baseline  
469 documents during Phase 1 of Blueprint Implementation. During Phase 2 of Blueprint  
470 Implementation, review and recommendation of Policy Baseline documents shall follow the  
471 process for a Policy Change as described in Section 10 of this MOU. During Phase 1 of  
472 Blueprint Implementation, the TJPA Project Director confirmed they will seek the  
473 recommendation of the IPMT for proposed Policy Baseline documents, and the TJPA Executive  
474 Director confirmed they will seek the review of the EWG for proposed Policy Baseline  
475 documents.

476

477

478 **9. Stage Gates:**

479

480 The Partners recognize the need to assess the Project's readiness to advance to subsequent  
481 major phases of delivery. The Project shall utilize a Stage Gate process to align decision-  
482 making at major milestones, ensure the completion of preceding tasks, consider the Project's  
483 readiness for successive phases of work, and provide for periodic review and advice.

484

FINAL

485 At each Stage Gate milestone, the Partners expect that the TJPA Board will consider granting  
486 approval to proceed to the next phase of the Project and will consider authorizing any specific  
487 associated actions. In preparation for a Stage Gate, the IPDT will prepare an assessment of  
488 Project readiness. In preparing Stage Gate recommendations, the TJPA Project Director  
489 confirmed they will seek the review and recommendation of the IPMT or CCB, and the TJPA  
490 Executive Director confirmed they will seek the review of the EWG.

491

492 The Stage Gate process will be invoked at the following project milestones:

493

494 **Stage Gate #1 – Procurement and Enabling Program:** Initiation of procurement of the  
495 project's Major Contracts, beginning with PDB/40-CT Request for Proposals.  
496 Procurement and delivery of the enabling program will also proceed.

497

498 **Stage Gate #2 – Pre-Construction:** Initiation of the pre-construction phase for the  
499 project's Major Contracts, beginning with PDB/40-CT.

500

501 **Stage Gate #3 – Construction:** Initiation of the construction phase of the Major  
502 Contracts, beginning with PDB/40-CT.

503

504 **Stage Gate #4 – Testing and Commissioning:** Initiation of testing and commissioning  
505 activities, including trial running of rail vehicles.

506

507 **Stage Gate #5 – Entry into Service:** Start of Revenue Service.

508

509 Section 3 of The Portal Governance Blueprint, provided as Attachment #1 to this MOU,  
510 presented the draft Stage Gate Framework for the Project, including anticipated precedent  
511 deliverables and milestones for each Stage Gate (with the exception of the separate Stage Gate  
512 for Testing and Commissioning, which has been added herein). Progression through the  
513 Project's Stage Gates 1, 2, and 3 may proceed in partial/progressive form at an individual Major  
514 Contract level, to reflect the differential schedules of individual Major Contracts.

515

516

517 **10. Change Decision Framework:**

518

519 The Partners recognize that the need for changes will occur throughout the delivery of the  
520 Project, including during procurement, construction, and testing and commissioning. The  
521 Partners also recognize that Project Changes should be controlled to ensure that the Project's  
522 planned outcomes are achieved and that the impacts of Project Change decisions are  
523 understood by the Partners.

524

525 Project Changes include modifications to configuration, schedule, budget, and/or contracts  
526 (including changes to contract scope, schedule, and cost). The following framework, as  
527 described in Section 4 of the Blueprint, will be used to categorize Project Change types:

528

FINAL

529 **Minor Change:** A Project Change that does not conflict with the Policy Baseline and is  
530 less than a defined threshold.

531

532 **Significant Change:** A Project Change that does not conflict with the Policy Baseline  
533 and that exceeds a defined threshold.

534

535 **Policy Change:** A Project Change that significantly alters or threatens the planned  
536 outcomes of the Project, or otherwise exceeds the defined threshold for a Policy  
537 Change, including all changes that are materially inconsistent with the Policy Baseline.

538

539 Specific thresholds for each level of Project Change shown above will be defined in the CCB  
540 Charter, as described in Section 7.5 of this MOU. The Partners anticipate that under the CCB  
541 Charter, Project Changes will generally follow the following processes for review,  
542 recommendation, and decision-making:

543

544 **Minor Changes:** Authority delegated by the TJPA Board to the TJPA Executive Director  
545 and from the Executive Director to the TJPA Project Director, or as otherwise delegated  
546 within the IPDT, with record of Minor Changes reported to the CCB.

547

548 **Significant Changes:** Reviewed and recommended by the CCB, with consideration of  
549 impact or compliance with the Policy Baseline. Authority delegated from the TJPA Board  
550 to TJPA Executive Director, with potential retention of authority by the TJPA Board for  
551 very large Significant Changes.

552

553 **Policy Changes:** TJPA Board retains approval authority. The TJPA Executive Director  
554 shall seek the review and recommendation of the CCB, and the TJPA Executive Director  
555 shall bring forward final recommendations to the TJPA Board. The TJPA Executive  
556 Director shall concurrently bring forward to the TJPA Board any recommended  
557 amendment or amendments to the Policy Baseline associated with a Policy Change.

558

559

560 **11. Project Status Reporting:**

561

562 The Partners recognize that timely, accurate, and accessible project information is essential to  
563 effective decision-making at all levels.

564

565 The IPDT will prepare a detailed Project Status Report monthly. The TJPA shall lead  
566 preparation of the Status Report. The TJPA Project Director will be responsible for the Report.  
567 The TJPA Project Director will present (or otherwise furnish) the Status Report to the IPMT or  
568 CCB. The TJPA Executive Director shall present (or otherwise furnish) a summary version of  
569 the Status Report to The Portal Committee, with the Report also made available to the full TJPA  
570 Board. During Phase 2 of Blueprint Implementation, the Project Director confirmed they will  
571 engage the IMT during the period of preparation of the Report. A draft of the Status Report will  
572 be provided to IMT members to support briefing of their originating organizations.

573  
574  
575  
576  
577  
578  
579  
580  
581  
582  
583  
584  
585  
586  
587  
588  
589  
590  
591  
592  
593  
594  
595  
596  
597  
598  
599  
600  
601  
602  
603  
604  
605  
606  
607  
608  
609  
610  
611  
612  
613  
614  
615

**12. Procedures for Decision Review, Recommendation, and Escalation:**

Section 6 of the Blueprint describes General Procedures for multi-agency coordination and engagement in decision review, recommendation, and escalation, as fully in place during Phase 2 of Blueprint Implementation. These General Procedures are incorporated by reference herein. In the event of inconsistency between the MOU and the Blueprint’s General Procedures, the MOU shall take precedence.

**13. Summary Work Program:**

The Partners recognize the need for documentation of the Project’s work program, to facilitate mutual understanding of Project activities and support each Partner’s own forward planning and resource allocation.

The Partners agree to prepare a Summary Work Program to describe the Project’s activities and Partner roles and responsibilities in these activities over a reasonable period (at least two years). The Summary Work Program shall be consistent with the Project work plan prepared and maintained by the IPDT. TJPA shall lead preparation and periodic update of the Summary Work Program; the TJPA Project Director confirmed they will request the input and cooperation of the IPMT or IMT. The TJPA Project Director confirmed they will seek the recommendation of the IPMT or IMT for the proposed Summary Work Program; the TJPA Executive Director confirmed they will seek the review of the EWG of the proposed Summary Work Program; and the Summary Work Program shall be presented to the TJPA Board.

The Summary Work Program shall be updated on an annual basis, in parallel with the Partners’ own processes to prepare and approve annual budgets, and presented to the TJPA Board. The TJPA Project Director confirmed they will present the draft Summary Work Program to the IPMT or IMT by March of each year, and the TJPA Executive Director confirmed they will present the draft Summary Work Program to the EWG by April of each year.

**14. Resourcing and Other Agencies:**

The Partners will work together to identify the necessary resources to support their respective responsibilities associated with delivery of the Project and participation in the activities of the bodies described in this MOU. This MOU does not commit any Partner to provide any resources beyond those that any individual Partner may have already committed to the Project and/or to their own associated activities. This MOU commits the Partners to participation in the processes described herein but does not constitute a commitment of financial resources.

## FINAL

616 The Partners recognize that other state, regional and local government agencies, such as  
617 BART, Capitol Corridor Joint Powers Authority, California State Transportation Agency, and  
618 Caltrans, have an interest in and/or expertise regarding the Project. Accordingly, the Partners  
619 agree to work collaboratively to engage those agencies as appropriate during implementation of  
620 the Project.

621  
622

623 **15. Other Agreements:**

624

625 The Partners acknowledge that there are other agreements already entered into by some or all  
626 of the Partners or which may be entered into in the future related to the Project or other related  
627 or unrelated matters, including but not limited to: bilateral agreements between TJPA and  
628 CCSF, between TJPA and Caltrain, and between TJPA and CHSRA; agreement(s) between  
629 Caltrain and CHSRA; and the Railyards MOU. This MOU is separate from and does not modify  
630 or replace any other MOU or other agreement to which one or more of the Partners is party.

631

632 Future agreements between or among two or more of the Partners concerning the Project  
633 cannot impair the rights and obligations of the parties as articulated in this MOU without the  
634 prior written consent of all parties to this MOU.

635  
636

637 **16. No Adjudication of Rights:**

638

639 The MOU does not adjudicate legal rights with respect to the development of the Project or  
640 provide the Partners with any rights with respect to the revenues derived therefrom.

641  
642

643 **17. General Conditions:**

644

645 17.1 Each Partner will conduct its activities under this MOU in accordance with applicable  
646 federal, state, and local laws, regulations, and standards.

647

648 17.2 Each Partner will ensure that personnel assigned by it to conduct activities under  
649 this MOU are appropriately qualified or licensed to perform the tasks assigned to them.

650

651 17.3 Each Partner will hold all administrative drafts and administrative final reports, studies,  
652 materials, and documentation relied upon, produced, created, or utilized for the activities under  
653 this MOU in confidence to the extent permitted by law. Where applicable, the provisions of  
654 California Government Code section 7921.505(c)(5) shall protect the confidentiality of such  
655 documents if said documents are shared between the Partners. The Partners will not distribute,  
656 release, or share said documents with anyone other than employees, agents, and consultants  
657 who require access to complete the activities under this MOU without the written consent of the  
658 Partner authorized to release them, unless required and authorized to do so by law. If a Partner  
659 receives a public records request pertaining to activities under this MOU, that Partner will notify

FINAL

660 the other Partners within five (5) working days of receipt and make the other Partners aware of  
661 any intent to disclose public documents. The Partners will consult with each other prior to the  
662 release of any public documents or statements related to the activities under this MOU. Nothing  
663 herein shall require any Partner to waive any attorney-client privileges or other protections it  
664 otherwise has a right to assert.

665  
666 **17.4** The Partners do not intend this MOU to create a third-party beneficiary or define duties,  
667 obligations, or rights of parties not signatory to this MOU.

668  
669 **17.5** The Partners will not assign or attempt to assign their rights or obligations under this MOU  
670 to parties not signatory to this MOU without an amendment to this MOU.

671  
672 **17.6** The following document is an Attachment hereto:

673 1. Policy Document: The Portal Governance Blueprint

674

FINAL

675 IN WITNESS WHEREOF, the Partners have executed this MOU as of the date first written  
676 above.

677  
678  
679

680 Transbay Joint Powers Authority

Metropolitan Transportation Commission

681

682

683

684

685

686

687

688

689

690

691

692

693

694

695

696

697

698

699

700

701

702

703

704

705

706

707

708

709

710

711

712

713


714

715

716


717


By:   
Jeff Gee, TJPA Board Chair

DocuSigned by:  
By:   
Andrew Fremier, Executive Director

Date: January 30, 2025  
Address: 425 Mission Street, Suite 250  
San Francisco, CA 94105

Date: 12/19/2024  
Address: 375 Beale Street, Suite 800  
San Francisco, CA 94105

San Francisco County Transportation Authority  
By:   
Tilly Chang, Executive Director

Peninsula Corridor Joint Powers Board  
By:   
Michelle Bouchard, Executive Director

Date: 1/14/2025  
Address: 1455 Market Street, Floor 22  
San Francisco, CA 94103

Date: 1/14/2025  
Address: 1250 San Carlos Avenue  
San Carlos, CA 94070

California High-Speed Rail Authority  
By: \_\_\_\_\_  
Ian Choudri, Chief Executive Officer

City and County of San Francisco  
By: \_\_\_\_\_  
Mayor London N. Breed

Date: \_\_\_\_\_  
Address: 770 L Street, Suite 620  
Sacramento, CA 95814

Date: \_\_\_\_\_  
Address: 1 Dr Carlton B Goodlett Pl  
San Francisco, CA 94102

FINAL

675 IN WITNESS WHEREOF, the Partners have executed this MOU as of the date first written  
676 above.

677

678

679 Transbay Joint Powers Authority

Metropolitan Transportation Commission

680

681

682 By: \_\_\_\_\_

By: \_\_\_\_\_

683 \_\_\_\_\_, TJPA Board Chair

\_\_\_\_\_, Executive Director

684

685

686 Date: \_\_\_\_\_

Date: \_\_\_\_\_

687 Address: 425 Mission Street, Suite 250  
688 San Francisco, CA 94105

687 Address: 375 Beale Street, Suite 800  
688 San Francisco, CA 94105

689

690

691

692

693

694 San Francisco County Transportation Authority

Peninsula Corridor Joint Powers Board

695

696

697 By: \_\_\_\_\_

By: \_\_\_\_\_

698 \_\_\_\_\_, Executive Director

\_\_\_\_\_, Executive Director

699

700 Date: \_\_\_\_\_

Date: \_\_\_\_\_

701 Address: 1455 Market Street, Floor 22  
702 San Francisco, CA 94103

701 Address: 1250 San Carlos Avenue  
702 San Carlos, CA 94070

703

704

705

706

707

708 California High-Speed Rail Authority

City and County of San Francisco

709

710

711 By:  \_\_\_\_\_

By: \_\_\_\_\_

712 Ian Choudri, Chief Executive Officer

Mayor \_\_\_\_\_

713

714 Date: November 19, 2024

Date: \_\_\_\_\_

715 Address: 770 L Street, Suite 620  
716 Sacramento, CA 95814

715 Address: 1 Dr Carlton B Goodlett Pl  
716 San Francisco, CA 94102

FINAL

IN WITNESS WHEREOF, the Partners have executed this MOU as of the date first written above.

Transbay Joint Powers Authority

Metropolitan Transportation Commission

**By:** \_\_\_\_\_  
Jeff Gee, TJPA Board Chair

**By:** \_\_\_\_\_  
Andrew Fremier, Executive Director

**Date:** \_\_\_\_\_  
**Address:** 425 Mission Street, Suite 250  
San Francisco, CA 94105

**Date:** \_\_\_\_\_  
**Address:** 375 Beale Street, Suite 800  
San Francisco, CA 94105

San Francisco County Transportation Authority

Peninsula Corridor Joint Powers Board

**By:** \_\_\_\_\_  
Tilly Chang, Executive Director

**By:** \_\_\_\_\_  
Michelle Bouchard, Executive Director


**Date:** \_\_\_\_\_  
**Address:** 1455 Market Street, Floor 22  
San Francisco, CA 94103

**Date:** \_\_\_\_\_  
**Address:** 1250 San Carlos Avenue  
San Carlos, CA 94070

California High-Speed Rail Authority

City and County of San Francisco

**By:** \_\_\_\_\_  
Ian Choudri, Chief Executive Officer

**By:**  \_\_\_\_\_  
Mayor London N. Breed

**Date:** \_\_\_\_\_  
**Address:** 770 L Street, Suite 620  
Sacramento, CA 95814

**Date:** 12/19/24  
**Address:** 1 Dr Carlton B Goodlett Pl  
San Francisco, CA 94102

## **ATTACHMENT #1**

**San Francisco Peninsula Rail Program  
The Portal: Downtown Rail Extension**

# **Governance Blueprint**

**August 2023**

## 1. Background and Context

The Downtown Rail Extension (DTX or The Portal) is Phase 2 of the Transbay Program, which is led by the Transbay Joint Powers Authority (TJPA). The Metropolitan Transportation Commission (MTC) and the San Francisco County Transportation Authority (SFCTA) have co-led The Portal Governance Study, in order to recommend the institutional arrangement and governance structure<sup>1</sup> through construction of the project, as described in Task 18 of the San Francisco Peninsula Rail Program Memorandum of Understanding (MOU). The MOU is a six-party agreement among the TJPA, the Peninsula Corridor Joint Powers Board (Caltrain), the California High-Speed Rail Authority (CHSRA), the City and County of San Francisco (CCSF), MTC, and SFCTA (collectively, Partner Agencies and individually, Partner Agency). The MOU defines a project development work program for The Portal and establishes the Integrated Program Management Team (IPMT) and the Executive Steering Committee (ESC), to undertake and guide this work program on behalf of the TJPA Board.

### Governance Study Approved Recommendations

In September 2022, the TJPA Board approved a set of governance recommendations for The Portal, as recommended by the ESC:

1. Confirm TJPA as the lead agency for DTX procurement and construction, and continue to build the capacity of TJPA and Partner Agencies for project delivery.
2. Develop a collaborative, integrated management approach and core management team, in order to support TJPA, align direction to the multi-agency delivery team, and actively manage risks and challenges.
3. Provide a transparent venue for the development and review of policy-level recommendations and reporting to the TJPA Board.
4. Utilize a stage-gate process to align decision-making at major milestones, ensure readiness for successive phases of work, and provide for periodic independent/expert review and advice.
5. Define/codify the governance and management structure through bi-lateral agreements between agencies, a successor to the existing Peninsula Rail Program MOU, and detailed program management plans.
6. Empower project leadership staff through delegated authorities, in conjunction with an integrated management approach and structured review/oversight processes.
7. Institute process/structure for management and oversight of configuration and change, including contractual changes.
8. Embed risk management and risk review at all levels, including policy oversight, technical management, and project execution.
9. Prepare “single-source” project reporting to provide timely and reliable information to management, partners, and decision-makers.
10. Develop an integrated project delivery team, including TJPA staff, consultants, and key Partner Agency resources/personnel, and pursue project partnering to strengthen collaboration.

---

<sup>1</sup> **Project Governance** means the organizational, oversight, and decision-making framework to direct and manage the project’s scope, schedule, budget, risks, and change.

The Governance Study recommendations were accompanied by a set of Governance Objectives for The Portal, as follows:

- *Clarity of Purpose* – Establish and maintain a clear focus on delivering the project.
- *Representation and Voice* – Provide project partners with voice and say, consistent with their project interests and risk ownership.
- *Responsiveness and Oversight* – Enable timely decision-making, and ensure proper direction and oversight of the project delivery team.
- *Capacity and Capabilities* – Deliver the project with expert resources with the required skills and capacity.
- *Accountability and Authority* – Provide decision-making authority in alignment with delegated accountabilities for project outcomes.
- *Transparency* – Give the public, stakeholders, and partners visibility into the project’s progress and opportunities for meaningful engagement.

### The Portal Governance Blueprint

The Portal Governance Blueprint (Blueprint) builds on the Governance Study recommendations approved in September 2022. The Blueprint further describes the recommended governance approach for the project through procurement, enabling program, pre-construction, construction, and commissioning (with these phases collectively referred to as “project delivery”). This Blueprint is intended to guide the preparation of a new MOU among The Portal Partner Agencies, to succeed the existing Peninsula Rail MOU that has governed the project during the procurement-readiness work program.

This Blueprint focuses on the broad structure for multi-agency collaboration across The Portal Partner Agencies and does not address individual agencies’ commitments, responsibilities, and decision rights. Multiple bi-lateral agreements between TJPA and Partner Agencies will be developed to enable implementation of The Portal. These include the Caltrain Master Cooperative Agreement (MCA) and the CCSF Interagency Cooperation Agreement (ICA). Caltrain’s role in the project, as first operator, will be described in the MCA.

The Blueprint was prepared by MTC and SFCTA, in cooperation with the IPMT and with guidance from the ESC.

### Organization of this Document

The Blueprint provides recommendations in the following five areas:

- Governance Structure and Bodies
- Policy Baseline and Stage Gate Framework
- Change Decision Framework
- Project Reporting Approach
- General Procedures for Decision-Making and Recommendations

This Blueprint addresses each of these topics and closes with a discussion of follow-up activities to implement the recommended governance model.

## 2. Governance Structure and Bodies

Section 2 of the Blueprint presents the overall recommended governance structure for project delivery and describes recommended parameters for each of the new governance bodies.

This Section provides the structure underpinning subsequent sections of the Blueprint. Section 3 and Section 4 describe, respectively, the recommended frameworks for policy decision-making and change decision-making, which the governance bodies are intended to facilitate and fulfill. Section 5 presents the recommended approach to the flow of project reporting across the bodies. Finally, Section 6 of the Blueprint describes recommended procedures for decision-making at each level of project governance.

### Governance Structure

The September 2022 governance recommendations reflected an indicative structure with multiple governance bodies. The Blueprint recommends a refined governance structure for project delivery, as shown in Figure 1, below.


Table 1, below, provides an overview of each of the governance bodies.

**Table 1. Summary Description of Governance Bodies**

Body	Description
TJPA Board	Policy body with decision authority for the project
The Portal Board Committee	Standing Committee of the TJPA Board, providing transparent and dedicated venue for review and recommendation to the TJPA Board of policy matters
Executive Working Group	Group of senior executives representing the Partner Agencies, convened by the TJPA Executive Director, providing advice and recommendations to the TJPA Executive Director and, through the TJPA Executive Director, to The Portal Board Committee
Change Control Board	Multi-agency body reviewing and recommending changes in project scope, schedule, budget, and contracts, informed by the project’s risk management program
Integrated Management Team	Senior management group supporting active management of project delivery, led by The Portal Project Director
Project Delivery Team	Integrated team of TJPA Staff, Consultants, and Partner Agency Resources

The immediately following sub-sections present recommended parameters for The Portal Board Committee, the Executive Working Group, the Change Control Board, and the Integrated Management Team. Subsequent sections of the Blueprint elaborate the functions, decision frameworks, and relationships of these bodies.

Figure 1. Recommended Governance Structure for Project Delivery

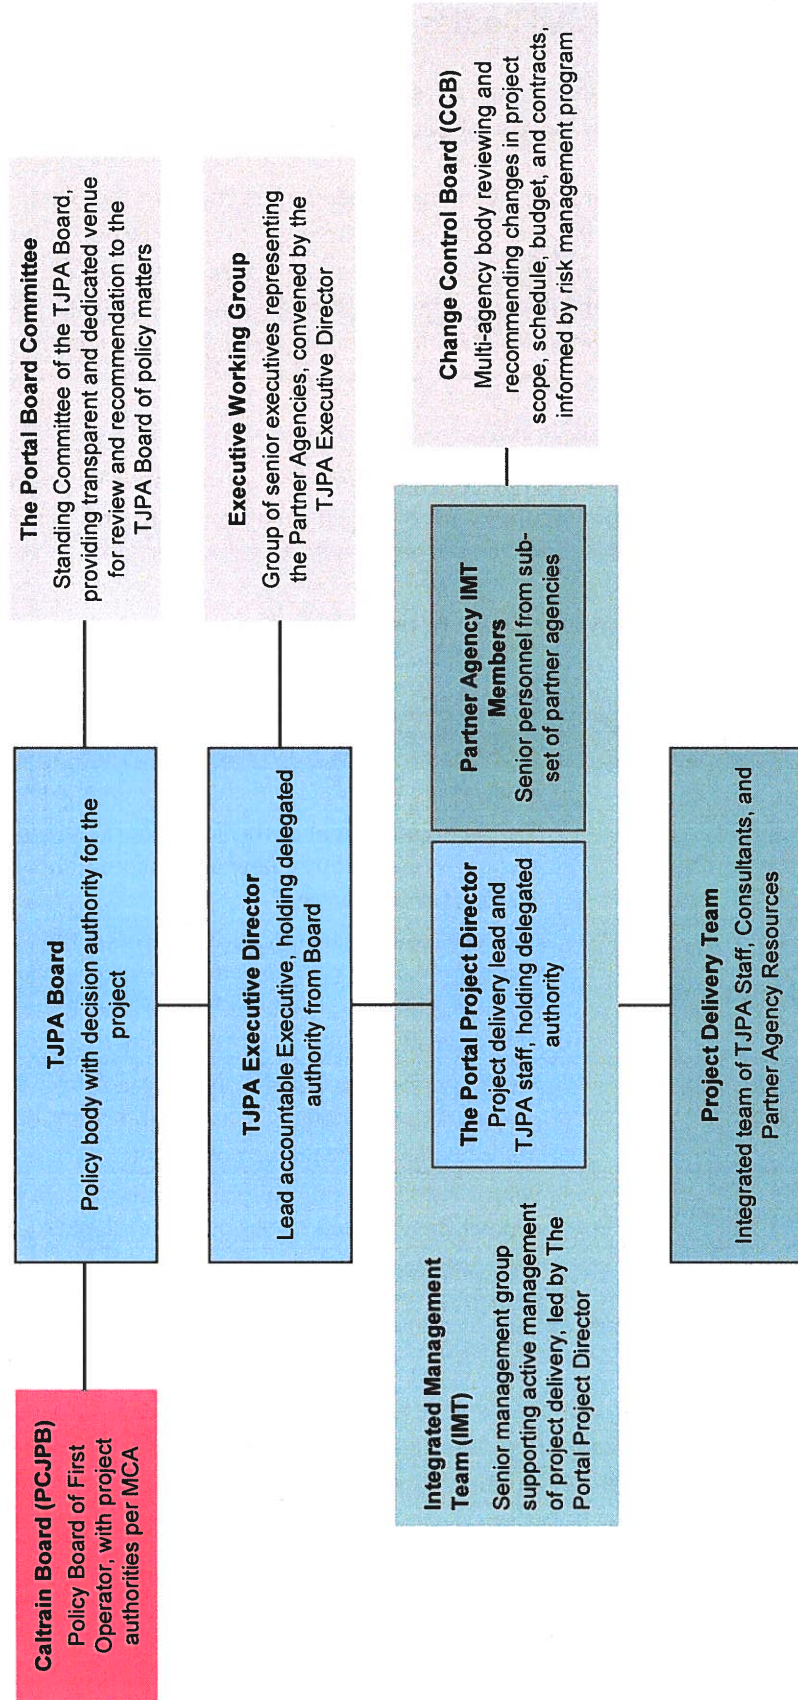

**The Portal Board Committee**

The TJPA Board holds decision authority on all matters related to The Portal project, including policy matters. The September 2022 governance recommendations called for the provision of “a transparent venue for the development and review of policy-level recommendations and reporting to the TJPA Board.”

The Blueprint recommends the establishment of a standing committee of the TJPA Board, referred to as The Portal Board Committee. The Committee would be responsible for reviewing, considering, and recommending Board-level policy matters. As a standing committee of the TJPA Board, The Portal Board Committee would hold meetings governed by the Brown Act.

Table 2, below, presents recommended parameters for The Portal Board Committee.

**Table 2. The Portal Board Committee**

<b>Primary Role/Function</b>	<ul style="list-style-type: none"> <li>Focused policy review, making recommendations to the full TJPA Board for final action</li> </ul>
<b>Supporting Role/Function</b>	<ul style="list-style-type: none"> <li>Conduct oversight of project management and project performance</li> </ul>
<b>Membership</b>	<ul style="list-style-type: none"> <li>To include three voting members</li> <li>To include representation from Caltrain and San Francisco</li> <li>To include MTC as a non-voting member</li> </ul>
<b>Provides Reports/Recommendations to:</b>	<ul style="list-style-type: none"> <li>TJPA Board</li> </ul>
<b>Receives Reports/Recommendations From:</b>	<ul style="list-style-type: none"> <li>TJPA Executive Director and Project Director (through TJPA Executive Director)</li> <li>Executive Working Group (through TJPA Executive Director)</li> <li>Change Control Board (through TJPA Executive Director)</li> </ul>
<b>Meetings</b>	<ul style="list-style-type: none"> <li>Meetings governed by the Brown Act</li> </ul>
<b>Documentation</b>	<ul style="list-style-type: none"> <li>Brown Act requirements</li> <li>Formal meeting minutes</li> </ul>

**Executive Working Group**

The Blueprint recommends the formation of an Executive Working Group, to facilitate multi-agency collaboration and project support at the executive level. The Group would consist of the Executive Director (or their designee) from each of the Partner Agencies.

The Executive Working Group would be convened by the TJPA Executive Director and would support the executive-level management of the project. The Group would also be responsible for providing policy

review support to The Portal Board Committee (through the TJPA Executive Director). The Executive Working Group meetings would not be governed by the Brown Act.

Table 3, below, presents recommended parameters for the Executive Working Group.

**Table 3. Executive Working Group**

<b>Primary Role/Function</b>	<ul style="list-style-type: none"> <li>• Support the executive-level management of the project; solicit, discuss, and apply best practices and lessons learned</li> <li>• Provide policy review/oversight support to the TJPA Executive Director, and support the TJPA Executive Director’s reporting to the Board Committee, including review of action items advancing to the Committee</li> </ul>
<b>Supporting Role/Function</b>	<ul style="list-style-type: none"> <li>• Review/resolve issues escalated from the Project Director / IMT</li> </ul>
<b>Membership</b>	<ul style="list-style-type: none"> <li>• Executive Director (or designee) from the six Partner Agencies</li> <li>• Convened by, and under the authority of, the TJPA Executive Director; all members may agendaize items for the Working Group’s consideration</li> </ul>
<b>Provides Reports/Recommendations to:</b>	<ul style="list-style-type: none"> <li>• TJPA Executive Director and the Board Committee (through the TJPA Executive Director)</li> </ul>
<b>Receives Reports/Recommendations From:</b>	<ul style="list-style-type: none"> <li>• Project Director / IMT (through the TJPA Executive Director)</li> <li>• Change Control Board (through the TJPA Executive Director)</li> </ul>
<b>Meetings</b>	<ul style="list-style-type: none"> <li>• Typical quarterly meeting frequency, with additional meetings as necessary</li> <li>• Meetings not governed by the Brown Act</li> </ul>
<b>Documentation</b>	<ul style="list-style-type: none"> <li>• Record of deliberations and recommendations, including representation of minority views when applicable</li> </ul>

**Change Control Board**

The Blueprint recommends the formation of a Change Control Board (CCB), with this body reviewing and recommending changes in project scope, schedule, budget, and contracts, including contractual and configuration changes, informed by the project’s risk management program.

Risk management and contingency management are functions closely related to the management of project changes. Certain change decisions reflect the materialization of project risks, and change decisions will often draw on contingency funds. As such, the Blueprint recommends that the CCB receive and review project risk reporting on a regular basis. The CCB should also receive timely reporting on budget and contingency.

The CCB would have representation from The Portal’s Partner Agencies. The Blueprint does not make detailed recommendations regarding voting procedures for the CCB; such detailed procedures should be codified in the Successor MOU. At the level of principles, the Blueprint recommends the following:

- The CCB should strive for consensus decision-making on whether to recommend a proposed change.
- Decision procedures on whether to recommend a proposed change should provide for clear escalation pathways to resolve conflict. TJPA Executive Director should not approve changes that are not recommended by the CCB; TJPA Board reserves authority to approve changes that are not recommended by the CCB, subject to transparency at the Board level regarding CCB position and Partner Agencies reservation of rights to impose consequences related to Board-approved changes that are not recommended by CCB.
- CCB decision-making on whether to recommend a proposed change should respect the differential risk profile and risk ownership of individual agencies (e.g., TJPA as lead agency and FTA grantee; Caltrain as first operator; CHSRA as future operator; funding agencies holding financial risk; and CCSF as host jurisdiction and as owner/operator of certain existing assets and future/project assets such as streets and utilities; etc.).

Table 4, below, presents recommended parameters for the CCB.

**Table 4. Change Control Board**

<b>Primary Role/Function</b>	<ul style="list-style-type: none"> <li>• Review and recommend changes in project scope, schedule, budget, and contracts, including changes to configuration and contracts, informed by the project’s risk management program</li> <li>• Monitor changes implemented below CCB approval thresholds</li> </ul>
<b>Supporting Role/Function</b>	<ul style="list-style-type: none"> <li>• Provide external input and advice to Risk Management Team: regularly review risk reporting, including project risk register; participate in quarterly risk workshops</li> <li>• Support identification of policy matters requiring consideration by other governance bodies</li> <li>• Provide staff-level review of items advancing to Executive Working Group</li> </ul>
<b>Membership</b>	<ul style="list-style-type: none"> <li>• Composed of senior technical representation from the Partner Agencies</li> <li>• FTA PMOC invited to attend meetings</li> <li>• Chair and Vice Chair elected by membership</li> </ul>
<b>Provides Reports/Recommendations to:</b>	<ul style="list-style-type: none"> <li>• Project Director / Integrated Management Team (for escalation to the TJPA Executive Director, Board Committee, and TJPA Board, as appropriate)</li> <li>• Executive Working Group (through the TJPA Executive Director)</li> </ul>
<b>Receives Reports/Recommendations From:</b>	<ul style="list-style-type: none"> <li>• Project Director / Integrated Management Team</li> </ul>
<b>Meetings</b>	<ul style="list-style-type: none"> <li>• The CCB should meet at least monthly, with the initial CCB group to recommend a proposed meeting structure/cadence</li> <li>• Meetings not governed by the Brown Act</li> </ul>
<b>Documentation</b>	<ul style="list-style-type: none"> <li>• Written record of CCB decision-making</li> <li>• Reports/recommendations to other bodies, as required or requested</li> </ul>

### Integrated Management Team

The Blueprint recommends the formation of an Integrated Management Team (IMT), to support TJPA in the active management of project delivery. The IMT would consist of senior managers from a subset of the Partner Agencies with the basis/need and capacity to participate at this level of project management. The IMT is intended to integrate/coordinate management-level activities across the agencies; to remove roadblocks and marshal resources; and to provide early/ongoing visibility into project status, issues, and risks.

The IMT would be led by the TJPA Project Director, and non-TJPA members would hold dual reporting obligations with the project and their home organizations. The IMT as a group would not have direct decision authority. Certain IMT member agencies will have specific decision rights established through bilateral agreements with TJPA. The IMT’s processes and procedures should be consistent with such agreements, including the Caltrain MCA and the CCSF ICA.

Table 5, below, presents recommended parameters for the IMT.

**Table 5. Integrated Management Team**

<b>Primary Role/Function</b>	<ul style="list-style-type: none"> <li>Integrate/coordinate activities and commitments across agencies</li> <li>Solve problems, remove roadblocks, and marshal resources</li> <li>Align direction to the Project Delivery Team</li> </ul>
<b>Supporting Role/Function</b>	<ul style="list-style-type: none"> <li>Support management of risks and issues</li> <li>Provide input to regular project reporting</li> </ul>
<b>Membership</b>	<ul style="list-style-type: none"> <li>Led by Project Director, with senior management-level representation from a subset of Partner Agencies with the basis/need and capacity for participation</li> </ul>
<b>Provides Reports/Recommendations to:</b>	<ul style="list-style-type: none"> <li>Executive Working Group (through the TJPA Executive Director)</li> <li>Members hold dual reporting to their home organizations</li> </ul>
<b>Receives Reports/Recommendations From:</b>	<ul style="list-style-type: none"> <li>Project Delivery Team (through the TJPA Project Director)</li> </ul>
<b>Meetings</b>	<ul style="list-style-type: none"> <li>Regular meetings, to provide timely visibility into project activities and facilitate project management integration</li> <li>Meetings not governed by the Brown Act</li> </ul>
<b>Documentation</b>	<ul style="list-style-type: none"> <li>Summary meeting notes reflecting outcomes and action items</li> <li>Reports/recommendations to other bodies, as required or requested</li> </ul>

### 3. Policy Baseline and Stage Gate Framework

A critical function of The Portal project governance model will be to control the project scope, budget, and outcomes throughout delivery. Section 3 of the Blueprint recommends the use of a Policy Baseline and a Stage Gate Framework to help structure and focus policy-level decision-making, in support of the delegation of management-level decision-making.

#### Policy Baseline

The Blueprint recommends that a Policy Baseline be established, with this Policy Baseline controlled by the TJPA Board. The Policy Baseline should describe the scope, schedule, budget, funding plan, and risk allocation for the project. The Policy Baseline should be consistent with the full/complete Project Baseline prepared for the Federal Transit Administration (FTA).

A limited set of Policy Baseline documents is recommended, with these documents drawing on existing project documents where applicable. Table 6, below, describes each of the recommended Policy Baseline documents.

**Table 6. Policy Baseline Documents**

Document	Basis	Description
Policy Baseline Project Definition	<ul style="list-style-type: none"> <li>Existing documentation, including approved environmental documents and material prepared for the Federal Transit Administration (FTA)</li> <li>Design criteria/requirements</li> <li>Service plan</li> </ul>	Summary description of the project scope, including project objectives, major design requirements, overall configuration, and service plan for revenue service.
Policy Baseline Schedule	<ul style="list-style-type: none"> <li>Master Schedule</li> </ul>	Milestone schedule indicating target dates of major milestones, consistent with the Master Schedule.
Policy Baseline Budget	<ul style="list-style-type: none"> <li>Detailed Project Budget</li> </ul>	Project budget describing expenditures at the level of major cost categories, consistent with the more detailed budget developed at an individual cost category level.
Policy Baseline Funding Plan	<ul style="list-style-type: none"> <li>20-Year Financial Plan</li> </ul>	The capital funding plan and operations and maintenance (O&M) funding plan.
Policy Baseline Risk Matrix	<ul style="list-style-type: none"> <li>Approved Project Delivery Strategy</li> <li>Project Risk Register</li> </ul>	Matrix describing major risks and risk categories, with planned risk ownership/allocation and mitigation approach.

Policy Baseline documents should be established through action of the TJPA Board. Subsequent changes to Policy Baseline documents would also be matters of TJPA Board decision-making. The Caltrain Board should also have a role in the Policy Baseline as appropriate and agreed.

Actions that are materially inconsistent with the Policy Baseline would generally be matters of policy-level decision-making. At project Stage Gates (as discussed below), the Policy Baseline should be reviewed and updated as required.

### Stage Gates

The September 2022 governance recommendations called for the utilization of “a stage-gate process to align decision-making at major milestones, ensure readiness for successive phases of work, and provide for periodic independent/expert review and advice.”

Each Stage Gate should have a limited set of expected precedent deliverables or milestones. At each Stage Gate, an assessment of project readiness should be prepared by the Project Delivery Team, with input and review from supporting governance bodies. Ultimately, the TJPA Board would grant approval to proceed to the next phase of the project and authorize any specific associated actions as required. Certain Stage Gate milestones may require precedent or concurrent decision-making by other agencies or parties (e.g., FTA, Caltrain, etc.).

The Blueprint identifies an initial Stage Gate framework, as shown in Figure 2, below. This framework is organized around the following project milestones:

- Stage Gate #1 – Procurement and Enabling Program: Initiation of procurement of the project’s Major Contracts, planned to begin with release of bid documents for the Progressive-Design Build (PDB) contract. Procurement and delivery of the Enabling Program will also proceed.
- Stage Gate #2 – Pre-Construction: Initiation of the Pre-Construction phase for the project’s Major Contracts, beginning with the PDB.
- Stage Gate #3 – Construction: Initiation of the Construction phase of the Major Contracts, beginning with the PDB.
- Stage Gate #4 – Operations: Start of revenue service.

The project’s advancement through Stage Gate #1 is scheduled to proceed under the existing Peninsula Rail MOU; the Successor MOU is planned to be in place for subsequent Stage Gate milestones. The Successor MOU should refine Stage Gates #2-4 and should define more detailed Stage Gate procedures, including review/decision processes and Partner Agency requirements.

Figure 2. Draft Stage Gate Framework



## 4. Change Decision Framework

Throughout the life of the project, including during procurement and construction, the need for changes will occur. These include changes from what was previously approved with respect to project configuration and project contracts. Project changes must be carefully controlled to ensure that the desired project scope is delivered and the impacts of change decisions on the rest of the project and its stakeholders are well understood. Section 4 of the Blueprint describes the framework for change decision-making, including a framework for Change Types and the broad recommended change process. During implementation of the Blueprint, a more detailed Delegated Authorities Framework should be prepared, including the establishment of specific thresholds for decision-making.

### Change Types

The Blueprint recommends that The Portal’s change management/decision process classify changes in three categories, as shown in Table 7, below.

**Table 7. Change Type Framework**

Change Type	Definition	Decision Process
<b>1. Minor Change</b>	A change that does not conflict with the Policy Baseline and is less than a defined threshold.	<ul style="list-style-type: none"> <li>TJPA Board delegates (through the TJPA Executive Director) to Project Delivery Team, with all changes reported to CCB (through TJPA Project Director and IMT)</li> </ul>
<b>2. Significant Change</b>	A change that does not conflict with the Policy Baseline and is more than a defined threshold.	<ul style="list-style-type: none"> <li>CCB reviews and recommends whether to approve changes</li> <li>TJPA Board delegates to TJPA Executive Director (and TJPA Project Director); Delegated Authorities Framework should consider thresholds for TJPA Board delegation to TJPA Executive Director or retention of authority by TJPA Board for very large Significant Changes.</li> </ul>
<b>3. Policy Change</b>	A change that significantly alters or threatens the planned outcomes of the project, including all changes that are materially inconsistent with the Policy Baseline.	<ul style="list-style-type: none"> <li>TJPA Board approves, with recommendation by CCB (through TJPA Executive Director)</li> <li>Where required: approval by other agency with decision authority, per governing agreements (e.g., MCA)</li> </ul>


### Change Decision Escalation Pathway

Changes may originate throughout the project organization including from stakeholder requests, revisions by the design team, and contractor requests. Regardless of the source, a member of the Project

**Delivery Team should be responsible for coordinating the change through the appropriate review and approval process, with changes documented using a consistent template.**

**Table 7, above, describes the recommended decision process for each change type. Figure 3, below, illustrates the typical escalation pathway for change decision-making, consistent with the recommended decision process. Procedures for change-related decision-making are further described in Section 6, below.**

**Figure 3. Change Decision Escalation Pathway**

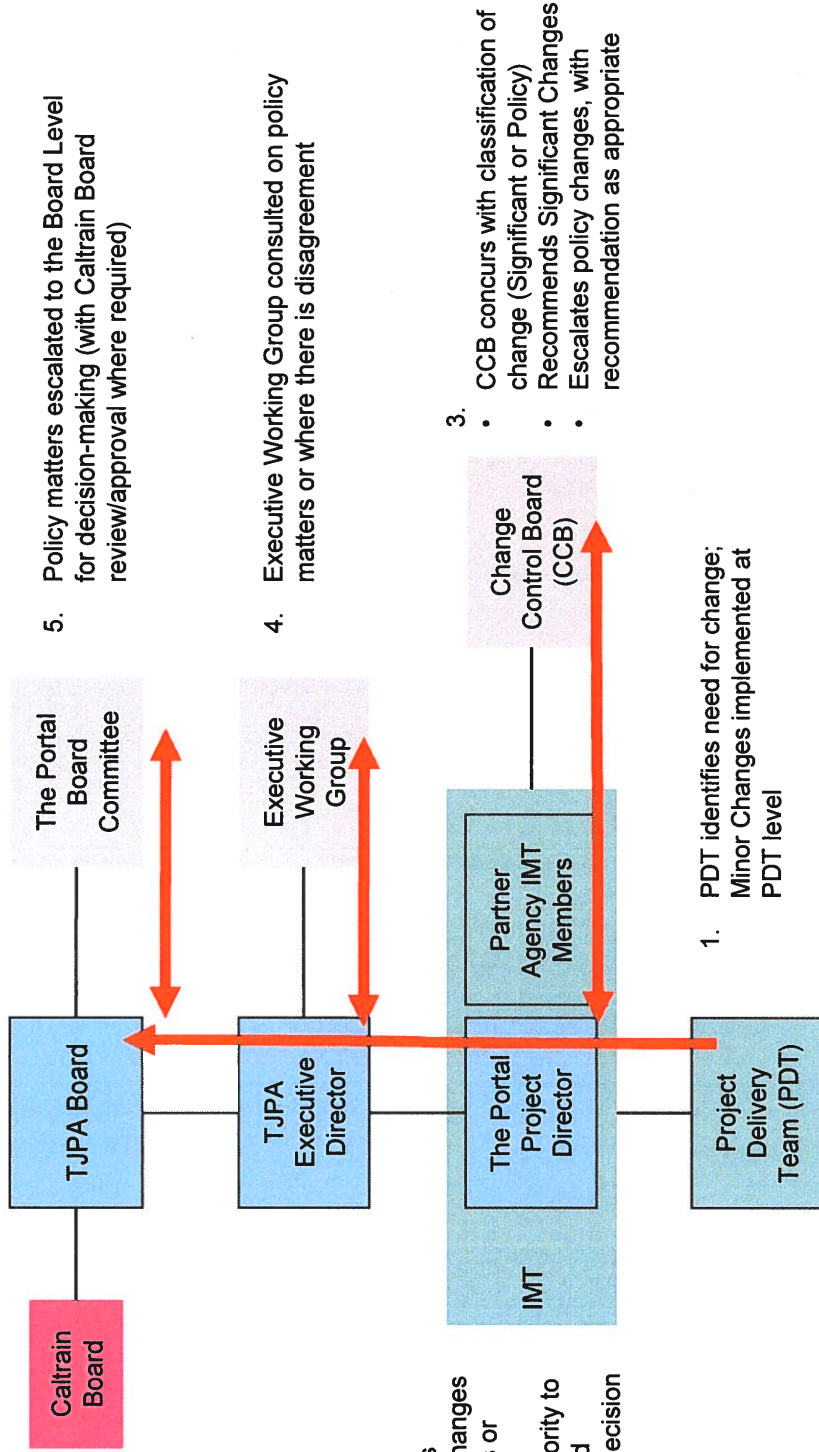

2. The Project Director has authority for all Minor Changes or Policy Changes, Project Director shall have authority to classify change type and forward to appropriate decision body.
  - For Significant Changes or Policy Changes, Project Director shall have authority to classify change type and forward to appropriate decision body.

3. CCB concurs with classification of change (Significant or Policy)
  - Recommends Significant Changes
  - Escalates policy changes, with recommendation as appropriate

5. Policy matters escalated to the Board Level for decision-making (with Caltrain Board review/approval where required)

4. Executive Working Group consulted on policy matters or where there is disagreement

1. PDT identifies need for change; Minor Changes implemented at PDT level

## 5. Project Reporting Approach

Timely, accurate, and accessible project information is essential to effective decision-making at all levels. Section 5 of the Blueprint provides recommendations with respect to flow of project information through the governance structure.

### Project Status Reporting


The Project Status Report should be consistent with the requirements of FTA and supplemented as necessary to meet the needs of The Portal's governance bodies.

Figure 4, below, illustrates the pathway for development and review of the Project Status Report. The key underlying principle is to have a single flow of information up from the Project Delivery Team to management-level and policy-level decision-makers, with input and review facilitated at each level.

A detailed Project Status Report will be prepared by the Project Delivery Team on a monthly basis. As shown in Figure 4, the Project Director and IMT will review the draft Status Report and provide input as required. The Project Director would be responsible for approving the report. The Project Director (or their delegate) will present the Status Report to the CCB; the CCB presentation should include any other material or information reasonably requested by the CCB to enable the body to fulfill its functions.

A summary version of the Status Report should be prepared and presented (through the TJPA Executive Director) to The Portal Board Committee (or otherwise provided to the Committee on months where the Committee does not meet), with this report also made available to the full TJPA Board (through the TJPA Executive Director).

Figure 4. Project Status Report: Development/Review Pathway

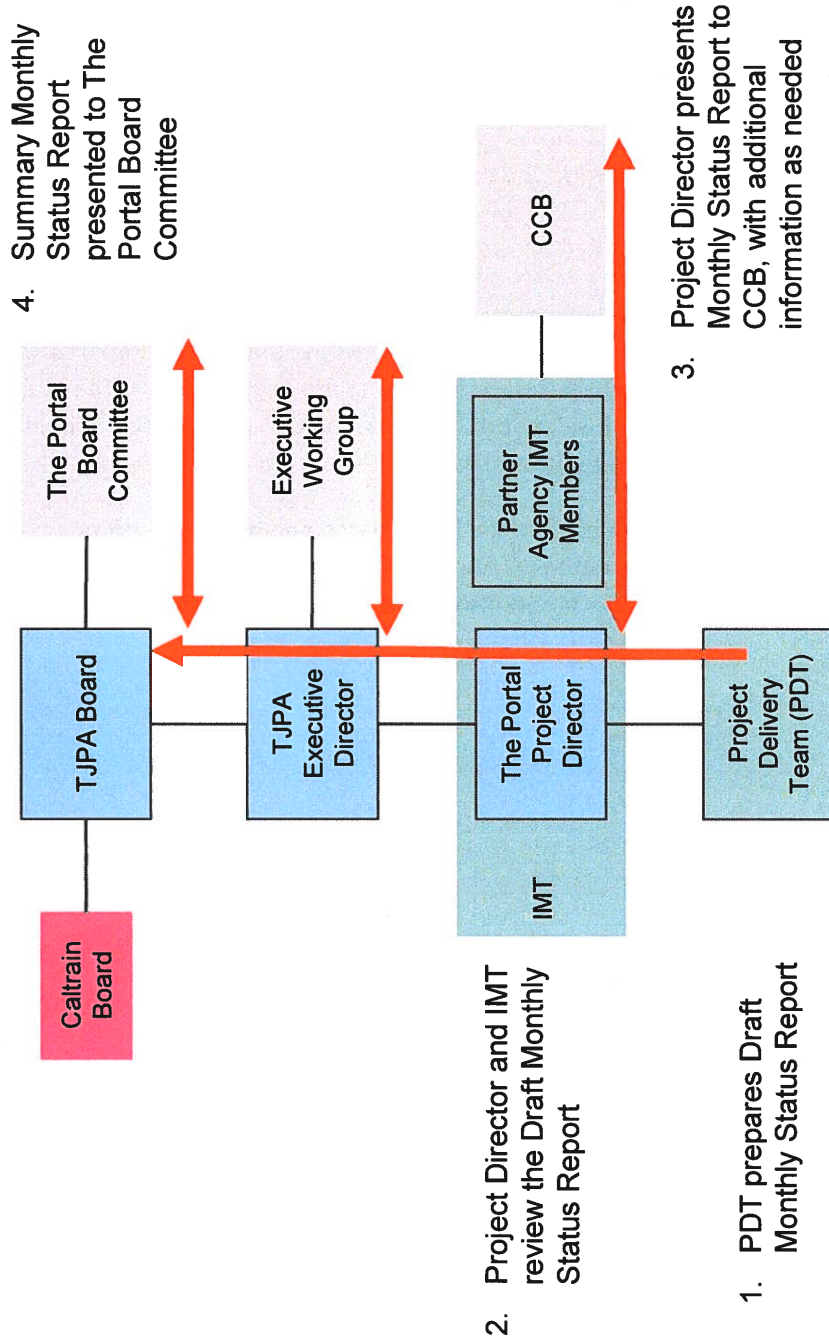

## 6. General Procedures for Decision-Making and Recommendations

Section 6 of the Blueprint describes recommended “General Procedures” for decision-making and/or recommendations at each level of the governance structure. These procedures integrate the recommendations of the above sections and are intended to provide overall guidance and expectations for the relationship of governance bodies to one another and the typical flow of decision-making on the project. In addition, the procedures include consideration of emergency situations and instances in which decision items may be advanced directly to the Board level.

### General Procedures: The Portal Project Director and Integrated Management Team

#### **The Portal Project Director and IMT:**

- The Project Director will be responsible for making project management decisions.
- The Project Director shall consult regularly with the Integrated Management Team (IMT), and the IMT shall advise and support the Project Director in management-level decision-making.
  - The Project Director shall be transparent with IMT and responsive to IMT member inquiries.
  - The IMT shall be readily available to advise and support the Project Director.
- Partner Agency IMT members shall have appropriate qualifications and shall be sufficiently dedicated to the project to keep pace with the project and its decision-making.
  - Partner Agency IMT members shall work to mobilize resources, decisions, and information from within their home organizations, to advance the project.
- Partner agencies shall retain all such authorities and decision rights that are provided for in relevant agreements, including the MCA and ICA.

### General Procedures: Change Control Board

#### **CCB:**

- Minor Changes approved and implemented at the PDT/PD level, with reporting to CCB (through the TJPA Project Director).
- The CCB will review and recommend Significant contract changes above agreed thresholds. Where Board approval is required, CCB recommendations will be provided by the TJPA Executive Director to the Board. The TJPA Executive Director will not approve changes that are not recommended by CCB. The TJPA Board may approve changes that are not recommended by CCB, if the CCB position is provided to Board and Partner Agencies reserve rights to impose consequences.
- The CCB will monitor changes approved below these thresholds.
- The CCB will review and recommend changes to configuration. Configuration changes that are of a policy nature shall be advanced to the Board level for approval.

**General Procedures: TJPA Executive Director and Executive Working Group**

**TJPA Executive Director and Executive Working Group:**

- The Executive Director will be responsible for bringing forward items to the Portal Board Committee and the full TJPA Board
- The Executive Working Group (EWG) shall be readily available to advise and support the Executive Director.
- The TJPA Executive Director shall either consult with or inform the EWG of decision items advancing to the Board Committee or full Board depending on the type and magnitude of the item at hand, generally distinguished as:
  - *EWG Consulted* – policy decisions, including approval/revision to Policy Baseline Documents, policy-level changes to contracts and configuration, dedication of program reserve funds, and other policy matters.
  - *EWG Informed* – non-policy decisions, including “Significant” contract changes, administrative matters, etc.
- Where the EWG is to be consulted, EWG review would generally occur through a meeting of the EWG. The EWG will convene on an immediate/urgent basis as necessary. The TJPA Executive Director may advance items directly to Board level if the EWG is unable to convene in a timely manner.
- The EWG will support resolution of disagreements and decision impasses at the IMT and CCB.

**General Procedures: TJPA Board and The Portal Board Committee**

**TJPA Board and The Portal Board Committee:**

- The Portal Board Committee (PBC) shall review proposed actions considered to be policy matters, including approval of (and revisions to) Policy Baseline documents, and make recommendations to the TJPA Board.
  - The PBC provides for a focused review of such matters, which are then referred to the full TJPA Board for approval.
- Board-level items/actions that are identified as non-policy matters may proceed directly to the TJPA Board for consideration/action. This would include:
  - Award/amendment of contracts that are consistent with the Policy Baseline;
  - Approval of very large Significant Changes, to the extent Board approval is required; and
  - Other administrative matters.

**General Procedures: Other Agency Boards**

**Other Agency Boards:**

- Items for which the Caltrain Board is the responsible or co-responsible decision authority (per the future MCA) shall require approval by the Caltrain Board.

- The Caltrain representatives to the IMT and EWG shall be responsible for working to facilitate this decision process, in coordination with TJPA staff.
- To the extent other Partner Agency Board decisions are required, an analogous process would be followed, with IMT/EWG representatives responsible for facilitating this process, working in coordination with TJPA staff.

**General Procedures: “Direct to Board” and Emergencies**

- “Direct to Board” and Emergencies:**
- The TJPA Executive Director retains the authority to directly bring forward decision items to The Portal Board Committee and/or the full TJPA Board at any time.
    - If an item is brought forward directly to the Board-level due to an emergency situation where delay is unacceptable, the TJPA Executive Director shall:
      - Identify the emergency situation in TJPA staff’s written report/memo to the Board;
      - Report back to the CCB and EWG in a timely fashion, with reconciliation decisions as required.
    - If EWG and/or CCB review has taken place, but the TJPA Executive Director brings forward a recommendation different from than the course of action recommended by EWG/CCB, this disagreement shall be noted in TJPA staff’s written report/memo to the Board.
  - In emergency situations (e.g., to protect health and safety), the Executive Director and Project Director shall have the responsibility and authority to take immediate required actions. In such cases:
    - The Executive Director shall promptly inform The Portal Board Committee Chair and the EWG.
    - The Project Director shall promptly inform the IMT.
    - TJPA Staff shall bring forward reconciliation decision items, where required, through normal processes, including documentation of the emergency situation and the rationale for taking immediate action.

## 7. Governance Implementation

The Portal project Partner Agencies should act quickly to establish the governance structure identified in the Blueprint. Section 7 briefly reviews key areas of follow-up work to pursue the recommendations of the Blueprint. Specifically, this section discusses the preparation of the Successor MOU; the development of the more detailed Delegated Authorities Framework; and considerations for the formation of new governance bodies.

### Successor MOU

The existing Peninsula Rail MOU is intended to bring the project to “ready-for-procurement” status. In Spring 2023, a time-only amendment of the MOU was executed, extending the term of the agreement to December 31, 2023.

To implement the Blueprint and govern multi-agency cooperation during project delivery, The Portal Partner Agencies should immediately initiate work to prepare, negotiate, and execute a new multi-party MOU (the Successor MOU) to succeed the Peninsula Rail MOU. The Successor MOU should codify the new governance structure and broadly describe the planned multi-agency work program for the project through construction and commissioning. Preparation of the Successor MOU should begin by developing and negotiating a draft term sheet by Fall 2023.

The Successor MOU should formalize Partner Agency agreement with the Delegated Authorities Framework discussed immediately below. The Successor MOU (and any future amendments to it) should also be aligned, as appropriate, with the project’s bilateral intergovernmental agreements, including the Caltrain MCA and CCSF ICA.

### Delegated Authorities Framework

A set of clear business rules is required to specify the use of delegated authorities and align with decision procedures at each level/body. Within these business rules, specific dollar/percentage value thresholds should be set for each change/action type. This Delegated Authorities Framework will require approval by the TJPA Board and should be incorporated into the Successor MOU. The Framework is recommended to reflect the following principles:

- The “Minor” dollar value threshold should be set high enough to allow for rapid decision-making on matters that are not related to policy and do not significantly impact the project budget.
- The CCB should have the ability to consider multiple change decisions together where those decisions stem from the same core issue as well as any decision that exceeds defined aggregate thresholds. Disputes related to classification of changes may be escalated to the Executive Working Group (through the TJPA Executive Director).
- The Delegated Authorities Framework should consider thresholds for TJPA Board delegation to TJPA Executive Director or retention of authority by TJPA Board for very large Significant Changes.
- The Framework should describe the approach to review/approve changes resulting in cost *savings*, including where such savings are the result of revised scope.
- Consideration of O&M cost impacts/savings should be provided for in cases where a contemplated change would have material impact on such costs.

- Changes requiring the use of Program Reserve funds shall require TIPA Board approval, regardless of nature or size.

### Formation of Recommended Governance Bodies

The establishment of the delivery-phase governance structure will require a transition and start-up period in order to form new governance bodies, implement/develop business processes, and build strong working relationships within and across governance bodies. The Portal Board Committee and its membership will be established through action of the TIPA Board.

The CCB should be in place as a body no later than the start of construction for the Enabling Program, which is scheduled to be underway in mid-2024. There is also the opportunity for the CCB group to begin convening at an earlier date in order to allow its membership to establish work practices and to provide input and review to the development of more detailed CCB business processes.

